

**GOVERNMENT OF INDIA
NORTH EASTERN COUNCIL SECRETARIAT
NONGRIM HILLS, SHILLONG – 793003**

Subject: Forwarding of Inspection Report.


In inviting a reference to the above subject, as requested by the concerned Sector, the physical inspection of the project "Construction/ Remodelling of RCC building including Development of Library, Vocational Centre etc. of Madhav Dev Higher Secondary School at Tulsimukh, Nagaon" was carried out on 27/06/2016. The inspection report duly signed by the Consultant (EE), NEC is enclosed herewith. The project was sanctioned on at a total cost of Rs.318.88 lakhs (NEC's share is Rs. 286.99 lakhs and State share is Rs. 31.88 lakhs). One installment of Rs. 115.00 lakhs was released by the NEC.

The inspection, inter alia, mentioned that:

- During inspection it could be seen that the progress of the work was very slow.
- It could be seen that construction of G+1 storied RCC building was not started yet.
- Construction of Cycle Stand already completed except painting works of truss and building portion and putting checkered tiles in the ramp section.
- During inspection it was found that total 261.65 m boundary wall constructed in the school compound area. It could be seen that finishing work at the top portion of the pillar of the boundary wall, installing MS Grill above the brick wall, painting works not yet completed.
- Construction of toilet block completed except painting works of truss and construction of two more wash basin. Total Plinth area of 38.13 sqm. was proposed in the approved DPR., but 35.874 sqm. toilet block was found constructed.
- NEC funding was not found to be acknowledged.

This is for information and necessary action by the concerned Sector.

Enclosure: As above.



(W. Synrem)
Economic Adviser (E&M)

U.O.No.NEC/EM/INSPECTION/HRD&E/2012

Dated: the 21.07.2018

To,
Director (HRD&E), NEC 

Copy to,

1. P.S to Planning Adviser, NEC for kind information of Planning Adviser 
2. PSA, NIC-NEC (Shri M. Nongkhlaw) for uploading the report with photograph on NEC website.

Report of the inspection carried on 09 / 02/2018 for the NEC funded project "Construction/Remodelling of RCC building including Development of Library,Vocational Centre etc.of Madhav Dev Higher Secondary School at Tulsimukh,Nagaon"

A joint inspection of the above project was carried out by an official of NEC Secretariat, Shillong and officials of the P.W.D., Govt.of Assam of on 09 /02/2018 at Guwahati Assam. The list of the officials present during the inspection is enclosed as Annexure-I, Photographs taken during the time of inspection are enclosed as Annexure-II .

(I) BACKGROUND:

Name of the project:	Construction/Remodelling of RCC building including Development of Library,Vocational Centre etc.of Madhav Dev Higher Secondary School at Tulsimukh,Nagaon
Location:	Tulsimukh,Nagaon
Implementing Agency:	Assam P.W.D.
Date of Sanction:	27/ 06 /2016
Cost of Project:	Rs.318.88 lakhs
NEC Share (90%):	Rs. 286.99 lakhs
State Share (10%):	Rs. 31.88 lakhs
NEC Share released & Dates:	1 st installment of Rs 115.00 lakhs on 27 / 06 /2016
Total Amount Released by NEC :	Rs. 115.00 lakhs
Balance amount to be released by NEC:	Rs. 171.99 lakhs
State Share released :	NIL
Balance amount to be released by State:	Rs. 31.88 lakhs
Status of UC for NEC share :	UC for Rs. 115.00 lakhs for 1st installment not yet submitted.
Status of UC for State share :	Not yet submitted
Target Date of Completion:	2(two)years from the date of sanction

(II)Aims/Objectives of the Project:- The proposed up-gradation of the infrastructure will provide educational boost for local people and provide proper arrangement as per demands and needs.

(III) Observations/ Status of works as on 09 / 02/2018 (Physical Achievements):-

Sl.No.	Description of Item	Amount approved by NEC (in Rs.)	Remarks based on site Inspection
1.	Construction of G+1 storied RCC school building	20672937.00	It could be seen that construction of G+1 storied RCC building was not started yet, it was also observed that half of the old school building structure already demolished. Implementing department informed that within this week pile work would be started in the demolished portion.
2.	Construction of Cycle Stand	642518.00	Construction of Cycle Stand already completed except painting works of truss and building portion and putting checkered tiles in the ramp section. It was found that Cycle Stand had been constructed as per approved DPR dimensions.
3.	Construction of boundary wall	2586050.00	During inspection it was found that total 261.65 m boundary wall constructed in the school compound. As per approved DPR total 265 m boundary wall was proposed. It could be seen that finishing work at the top portion of the pillar of the boundary wall, installing MS Grill above the brick wall, painting works not yet completed.
4.	Construction of low site raising by earth filling	781994.00	Not yet completed.
5.	Construction of Approach Road inside the school complex	504894.00	Not yet started.
6.	Construction of outside toilet block	1017483.00	Construction of toilet block completed except painting works of truss and construction of two more wash basin. Total Plinth area of 38.13 sqm. was proposed in

			the approved DPR., but 35.874 sqm. toilet block was found constructed.
7.	Repairing /Maintenance of existing Assam type building	257282.00	Not yet done.

Location: Tulsimukh,Nagaon

Latitude 26.246480⁰ N

Longitude 92.679998⁰ E

(IV) Overall Remarks and Suggestions:-





During inspection it was found that construction of G+1 storied RCC building was not started yet, it was also observed that half of the old school building structure already demolished. Construction of Cycle Stand already completed except painting works of truss and in building portion still remains. During inspection it was found that total 261.65 m boundary wall constructed in the school compound area. Construction of toilet block had been completed except painting works of truss and construction of two more wash basin was still left. For Toilet total Plinth area of 38.13 sqm. was proposed in the approved DPR., but 35.874 sqm. Toilet block was found constructed. NEC funding was not found to be acknowledged in the project location , no signboard stating all the details like name of the project, cost of the project, funded by, implemented by, date of commencement of work and date of completion etc. was not erected. The officials of the implementing agency were asked to do the needful for acknowledging NEC funding. The overall progress is very slow and the Principal of the school was quite unhappy because with the demolition of a section of the old building, there is now lesser accommodation for the different classes. The work has to progress at a faster pace so that students and teachers are not made suffer due to lack of proper infrastructure. It may take some more time before the implementing department can submit full UC for 1st installment and, as of now ,the question of releasing the 2nd installment from NEC does not arise.



Abhijit Sarkar)


(Consultant (EE), NEC Secretariat

List of officials who were present during the inspection of NEC funded project
 "Construction/Remodelling of RCC building including Development of Library, Vocational Centre
 etc. of Madhav Dev Higher Secondary School at Tulsimukh, Nagaon" on 09/02/2018


Sl. No.	Name	Contact No. & Email id	Designation & Organisation/Department	Signature
1.	Toseswar Saikia	9401091141 toseswarOsakia@gmail.com	Madhav Dev H.S. School, Tulsimukh Deptt. Education	
2.	Parvesh Nath	9435019680	E.E. P.W.D. Nagaon Bldg. division	
3.	Anupjyoti Borah	9435362418	A.E. P.W.D. Nagaon Building division	
4.	Abhijit Sarwan	8250569195	Consultant (EE) NRC, Silong	
5.				
6.				
7.				
8.				
9.				
10.				




View of Boundary Wall at Madhav Dev Higher Secondary School in Tulsimukh

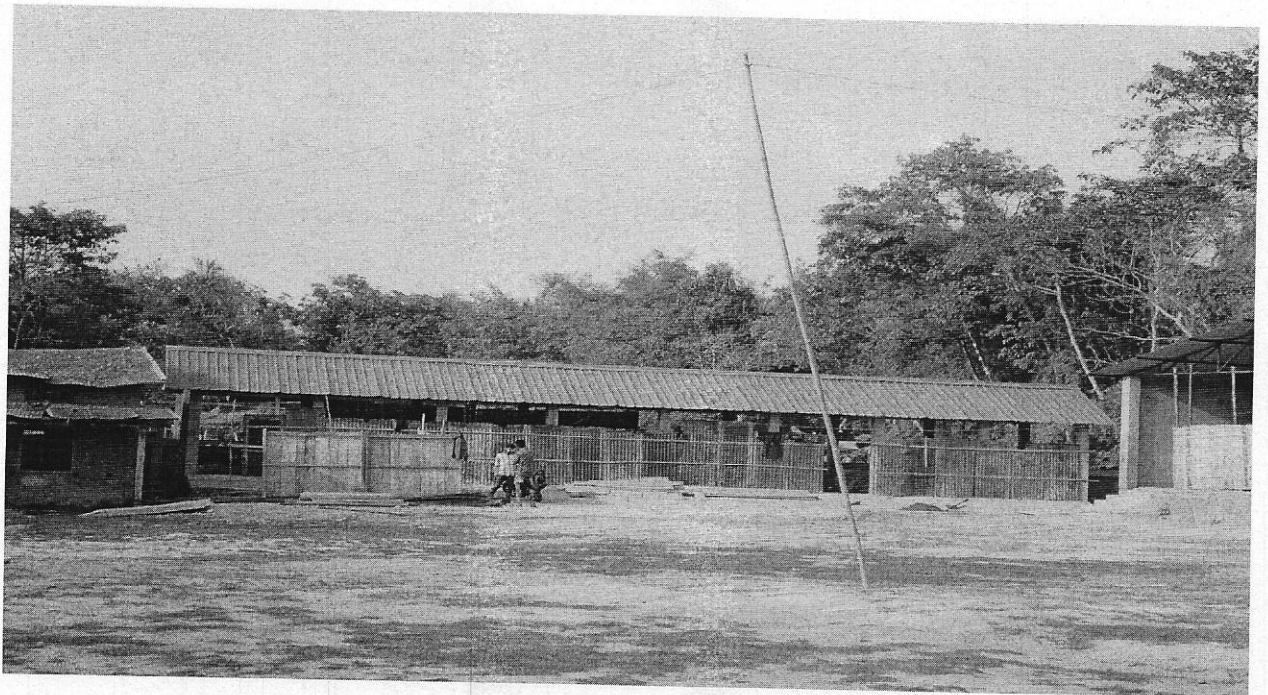


View of Cycle Stand at Madhav Dev Higher Secondary School in Tulsimukh

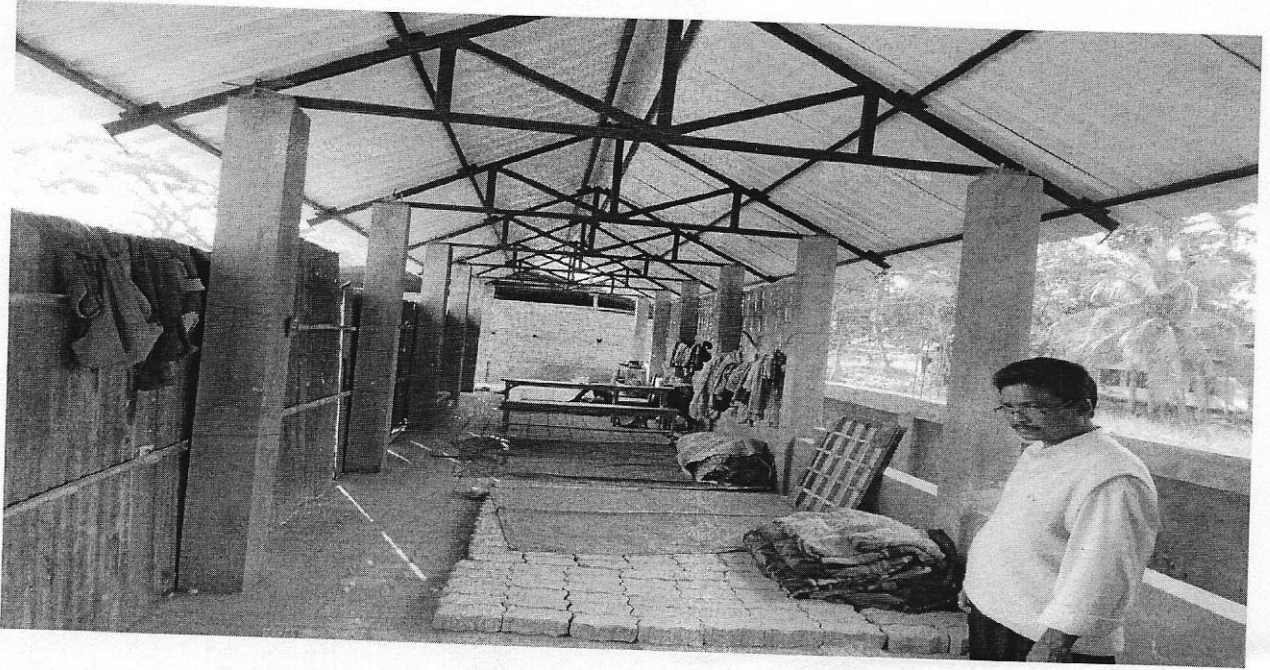


Inside view of Cycle Stand at Madhav Dev Higher Secondary School

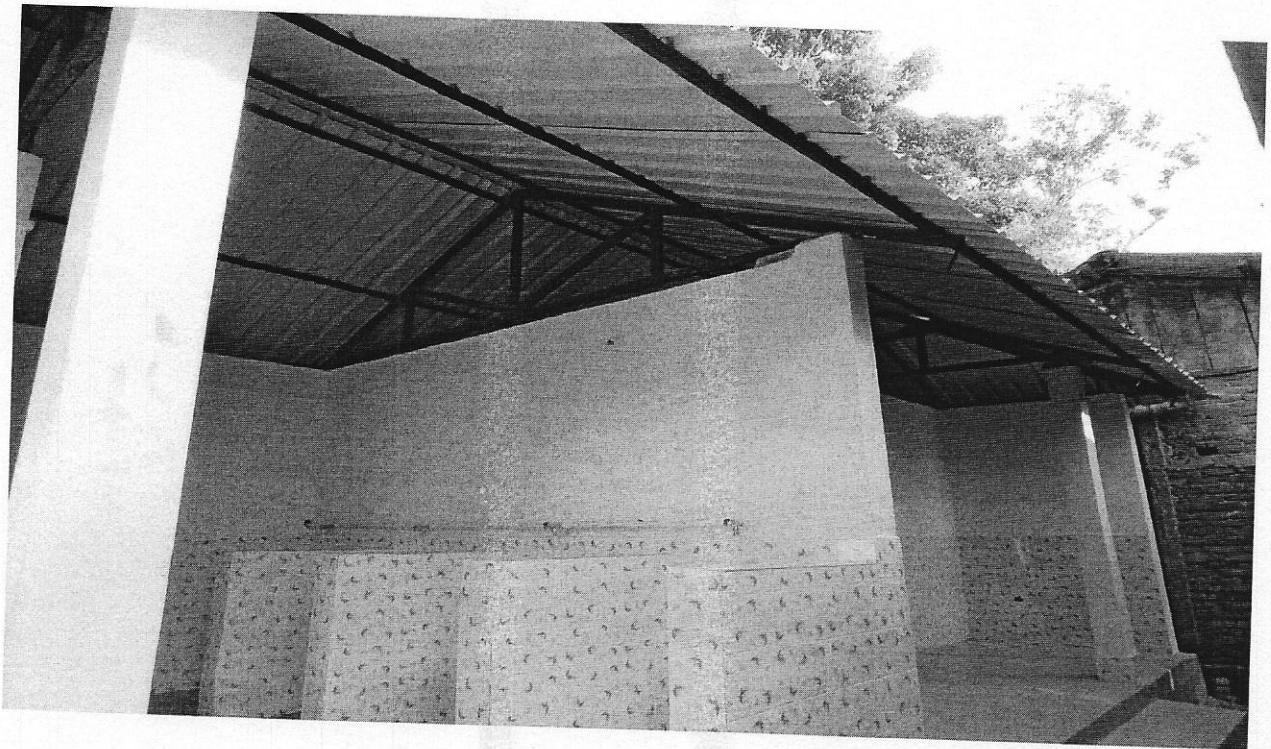

View of Toilet Block at Madhav Dev Higher Secondary School

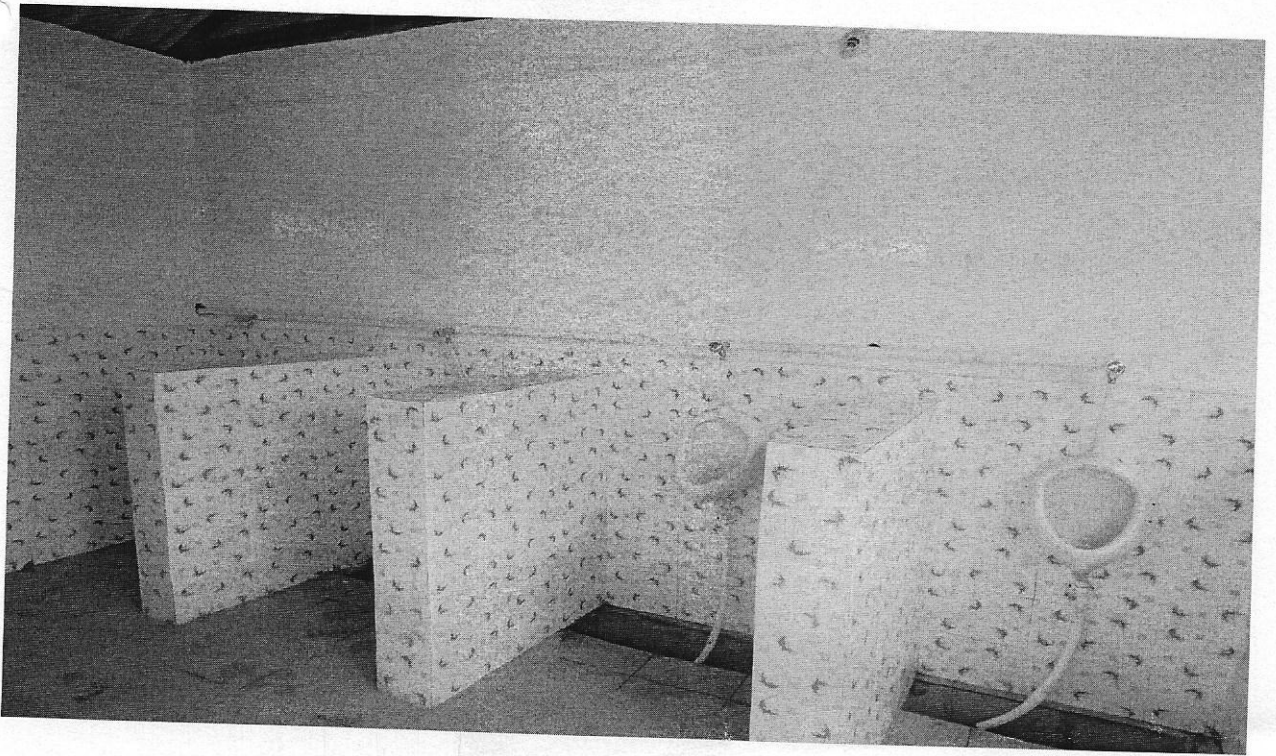


Inside view of Toilet Block at Madhav Dev Higher Secondary School

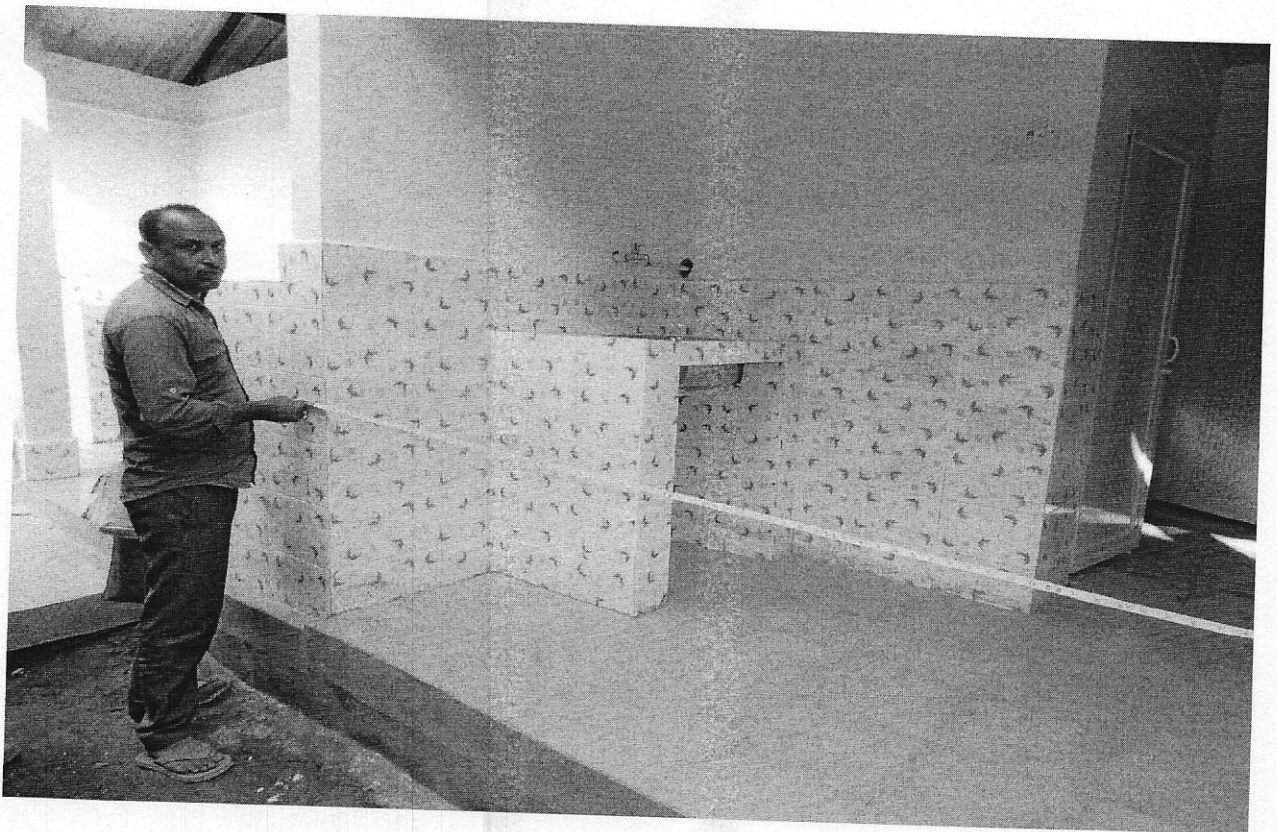

Mesurement taking at Toilet Block of Madhav Dev Higher Secondary School



Inspection Team in front of the Madhav Dev Higher Secondary School

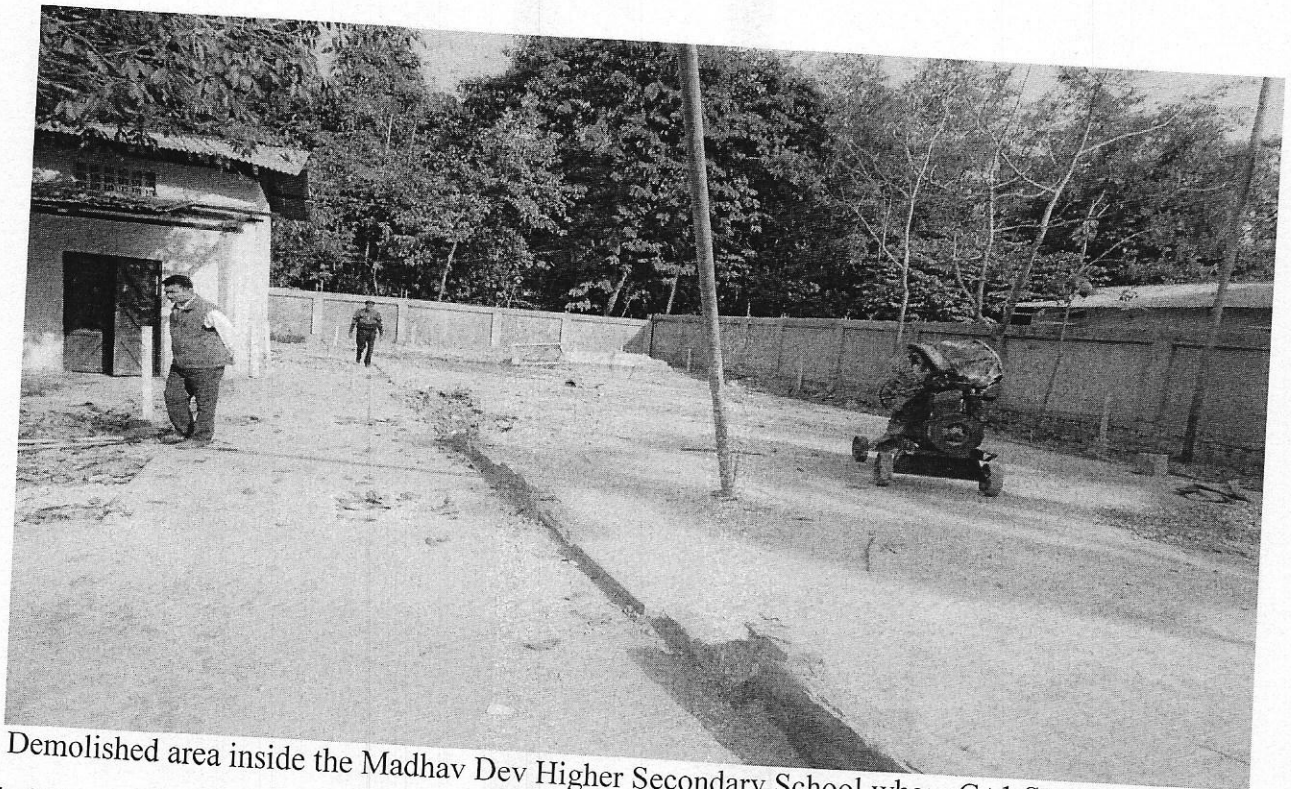

Demolished area inside the Madhav Dev Higher Secondary School where G+1 Storied schhol building will be constructed.
