

1/3151/2022

**GOVERNMENT OF INDIA
NORTH EASTERN COUNCIL SECRETARIAT
NONGRIM HILLS: SHILLONG - 793003**

Dated the:25th July, 2022

Subject: Forwarding of Inspection Report.

In inviting a reference to the above subject, and also as requested by the concerned Sector, the physical inspection of the project "**Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur**". Was carried out in, Chandel, Manipur on 22/06/2022. The inspection report duly signed by the Consultant(CE) & (ME) NEC is enclosed herewith. The project was sanctioned on 21-10-2020 at a total cost of Rs. 286.00 Lakh One installments totaling Rs. 114.00 Lakh Dated 21-10-2020 (40% of NEC Share) were released by the NEC.

The inspection, inter alia, mentioned that:

The Project is for Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur.

During inspection following observation were made:-

- The project was implemented in 20 locations in in Chandel District, Manipur.
- A total of 12 Components/ Construction scattered in 20 location was approved by NEC under the Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur. Out of which 16 components/project site were inspected. 4 (four) of the project site could not be inspected, 2(two) site due to inaccessible road condition and the other 2(two) as the work has not yet started.
- Based on the observations found at 16 location inspected, it can be said that the physical progress seems to commensurate with the financial progress.

(i) Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong (91.22 sq m)

- The works for the Teacher's Transit Quarter at SDO Office Complex, Chakpikarong is seen to be in progress , till date the progress of the construction works at site is 95 %. Earthwork, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
- Brickworks, plastering works, woodworks, steelworks, installation of windows, doors has been done at site.
- Finishing works like, painting works, flooring works is seen to be in progress.

I/3151/2022

- Internal electrification works has been done at site.
- Sanitary works, Water closet, HCl soil, waste and vent pipes , is left to be completed.
- The plinth area i.e **91.22 sq m** was found to be more or less **as per specification**

(ii) Construction of Teacher's Quarter at Sajik Tampak High School, Manipur. (77.69 sq m) mentioned in the approved DPR

- The works for the Teacher's Quarter at Sajik Tampak High School, Manipur is seen to be in progress, till date the progress of the construction works at site is 80 %. Earthwork, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage.
- Formworks, Brickworks, plastering has been done at site.
- Woodworks, steel works for doors and windows, plastering works, installation of windows, doors has not yet started.
- Finishing works like plastering works, painting works is yet to start.
- Sanitary works, internal electrification works is yet to start.
- The plinth area was measured to be around 86.50 sq m which is more than the plinth area i.e 77.69 sq m as per specification mentioned in the approved DPR.
- A signboard acknowledging NEC funding was not found at site

(iii) Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur. (77.69 sq m)

- The works for the Transit Quarter for Doctors' and Nurses at Phoikon, Manipur is seen to be in progress, till date the progress of the construction works at site is 75 %. Earthwork, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage.
- Formworks, Brickworks, plastering has been done at site.
- Woodworks, steel works for doors and windows, plastering works, installation of windows, doors has not yet started.
- Flooring works is seen to be in progress.
- Finishing works like plastering works, painting works is yet to start.
- Sanitary works, internal electrification works is yet to start.
- The plinth area was measured to be around 87.00 sq m which is more than the plinth area i.e 77.69 sq m as per specification mentioned in the approved DPR.

(iv) Construction of Primary School at Sugnu Tribal, Manipur. (217.68 sq m)

- The works for the Primary School at Sugnu Tribal, Manipur, has been completed, till date the progress of the works at site is 100 %. Earthwork, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .

1/3151/2022

- Brickworks, plastering works, woodworks for installation of windows, doors has been done at site.
- Steel works, roofing and ceiling works has been done at site.
- Finishing works like painting works, sanitary works, electrification works has been completed.
- The plinth area for the Primary School at Sugnu Tribal had to be reduced from **217.68 sq m (plinth area in the approved DPR) to 122.63 Sq m**. The implementing department informed that the reduction in the plinth area was due to the need of a toilet as there was no provision of toilet for the school. Extra works like construction of **toilet of plinth area 6.80 sq m** and water tank for the toilet has been carried out and completed. Sanitary works, internal electrification works is yet to start

(v) Construction of Multipurpose Hall at Langching Sec. School, Manipur. (243.92 sq m)

- The works for Multipurpose Hall at Langching Sec. School, Manipur, is seen to be in progress, till date the progress of the works at site is 80 %. Earthwork , structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
- Brickworks, woodworks for installation of windows, doors has been done at site.
- Steel works, roofing and ceiling works has been completed.
- Flooring works is seen to be in progress, Plastering works, finishing works and other miscellaneous works the implementing department informed that the work will be completed once the structural works is completed.
- Remaining finishing works like painting works, electrification works, and other miscellaneous, the implementing agency verbally informed that the remaining works will be started as soon as the structure is complete.
- The plinth area i.e 243.92 sq m was found to be as per specification mentioned in the approved DPR.
- There is a slight change in the orientation of the main door from centre as per the plan to the left corner as per requirements as informed by the implementing department. Extra work like provision of a stage was constructed inside the hall as per requirements and need

(vi) Water supply scheme at T Phailen, Manipur (27.00 sq m)

- The works for Water supply scheme at T Phailen, is seen to be completed, , the percentage progress of the works at site could not be determined although the work was completed as the construction of some of the components is not as per the approved DPR, Earthwork , structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .

I/3151/2022

- Brickworks, plastering works, formwork has been done at site.
- Vertical wall works, Roofing /ceiling works has been completed.
- The plinth area for the Water supply scheme is measured to be around 14.00 sq m which is very less as compared to the plinth area mentioned in the approved drawing in the approved DPR i.e 27.00 sq m

(vii) Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur (111.63 sq m).

- The works for Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur, is seen to be in progress, the percentage progress of the works at site is 97%. Earthwork ,structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
- Brickworks, plastering works, woodworks for installation of windows, doors has been done at site.
- Steel works, roofing and ceiling works has been done at site.
- Finishing works like painting works, sanitary works, electrification works is almost completed.
- Due to site restrictions the plinth area for the Classrooms had to be reduced from 111.63 sqm (plinth area in the approved DPR) to 90.00 sq m and accordingly there is a reduction of 2 nos of column from the original plan of the School, which is compensated with the additional construction of verandah and ramp of plinth area 18.11 sq m having 4 circular pillar has been carried out at the Kovol primary school with the total plinth area coming up to 108.11 sq m.

(viii) Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur (212.46 Rm)

- The works for barb wire fencing with gate at Khubung Khunou Primary School, Manipur, is seen to be completed, the percentage progress of the works at site is 100%.
- Earthwork ,formwork in foundation, footings, bases of columns, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
- Approximately 230 Rm of barb wire fencing with gate has been constructed which is more than the length given in the approved DPR i.e 212.46 Rm.

(ix) Construction of Public Toilet at Chakikarong Bazar, Manipur (6.94 sq m)

- The works for Construction of Public Toilet at Chakikarong Bazar, Manipur, is seen to be in progress, the percentage progress of the works at site could not be determined as the construction of some of the components is not as per the approved DPR.
- Earthwork ,structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done

/3151/2022

at the initial stage .

- Brickworks, plastering works, woodworks for installation of windows, doors has been done at site.
- Steel works, roofing and ceiling works has been done at site.
- Finishing works like painting works, sanitary works, electrification works is almost completed.
- No separate provision for Urinal was found at site, instead the urinal was found to be constructed in one of the toilets with no such partition or wall in between. The plinth area i.e 6.94 sq m was found to be more or less as per specification mentioned in the approved DPR

(x)Installation of borewell at 9 locations @ 4 lakhs per unit, Manipur

- The works for Installation of borewell at 9 locations, is seen to be in progress, the percentage progress of the works at site is around 78% installation of borewell is completed at 7 locations and it is found to be functional and catering to the need of the people in the area. For the remaining 2(two) installation work has not yet started
- Regarding aims and objective we can say that somehow the project was able to cater the need of the people in the village of Chandel District.the project which is committed to raising the living standards of its citizens and ensuring inclusive growth for all - "Sabka Saath Sabka Vikas aur Sabka Vishwas". While interacting with the villagers they express gratitude, for example the installation of borewell has help them tremendously. As water management and services is absolutely essential for eradication of poverty and is necessary condition for enabling sustained economic growth
- A signboard acknowledging NEC funding was not found at all the site. Therefore, the Implementing Department was asked to erect a permanent signboard stating that the project was funded by NEC.This is for kind information and necessary action by the concerned Sector

Signed by Mangsatabam
Iboyaima Meitei
Date: 25-07-2022 14:24:18
(Mangsatabam Meitei)
I/c Director (E&M)

Enclosure: As above.

To,

Adviser (Horticulture), NEC

Copy to,

1. P.A to Plg. Adviser, NEC for kind information of Planning Adviser, NEC.
2. Sr. T.D., NIC-NEC (Shri M. Nongkhlaw) for uploading the report with

1/3151/2022

photograph on NEC website.

GOVERNMENT OF INDIA
NORTH EASTERN COUNCIL SECRETARIAT
NONGRIM HILLS: SHILLONG – 793003

To
I/c Director (E &M)
North Eastern Council Secretariat
Nongrim Hill, Shillong.

Dated:- 06/07/2022

Subject: Submission of Inspection Report of NEC funded project titled "Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur".

We, Aarti Khyriemujat Consultant (CE) and Liza R Hek Consultant (ME) have done the Physical Inspection of the project "Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur". The project was sanctioned on 21-10-2020 at a total cost of Rs. 286.00 Lakh One installments totaling Rs. 114.00 Lakh Dated 21-10-2020 (40% of NEC Share) were released by the NEC under "MH 2552" to District Rural Development Agency Govt. of Manipur.

Objective of the Project:-

- a) Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur is to provide accommodation facility for Doctors and Nurses at PHC Sajik Tampak.
- b) Water supply scheme at T Phailen, Manipur is to provide tapped drinking water to at least 50 households in and around T Phailen Village.
- c) Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur is to provide secure existing primary school with aim to consolidate the existing infrastructure.
- d) Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong, Manipur is to provide transit accommodation facility to Government Teachers in and around Chakpikarong Sub-Division Hqtr. Area.
- e) Construction of Primary School at Sugnu Tribal, Manipur is to provide primary education at Sugnu Tribal area.
- f) Construction of Doctors' and Nurse Transit Quarter at PHSC Khubung Khullen, Manipur is to provide accommodation facility for Doctors and Nurses of PHSC Khubung Kullen.
- g) Construction of 2 additional Classrooms at Kovol Primary School, Tami, Chandel district is to provide additional classrooms to accommodate at least 40 more students.
- h) Installation of borewell at 9 locations/ village, Manipur is to provide tapped drinking water to water deficient villages.
- i) Construction of Public Toilet at Chakikarong Bazar, Manipur is to provide clean and improved sanitation facility at Chakpikarong Hqtr. Bazaar.
- j) Construction of Teacher's Quarter at Sajik Tampak High School, Manipur is to provide accommodation facility for teachers of Sajik Tampak High School, Sajik Tampak.

Liza R. Hek
Consultant (ME)
NEC, Sect

A. Khyriemujat
Consultant (CE)
NEC, Sect

- k) Construction of 2 additional Class rooms at Phiram Machet Primary School, Manipur is to provide additional classrooms to accommodate at least 30-40 students.
- l) Construction of Multipurpose Hall at Langching Sec. School, Manipur is to provide educational and recreational activities of Langching primary and secondary schools.

Indication of Works as per DPR:-

1. Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur is to provide accommodation facility for Doctors and Nurses at PHC Sajik Tampak
2. Water supply scheme at T Phailen
3. Construction of barb wire fencing with gate at Khubung Khunou Primary School
4. Construction of Teacher's Transit Quarter at SDO Office Complex
5. Construction of Primary School at Sugnu Tribal
6. Construction of Doctors' and Nurse Transit Quarter at PHSC Khubung Khullen
7. Construction of 2 additional Classrooms at Kovol Primary School, Tami
8. Installation of borewell at 9 locations/ village
9. Construction of Public Toilet at Chakikarong Bazar
10. Construction of Teacher's Quarter at Sajik Tampak High School
11. Construction of 2 additional Class rooms at Phiram Machet Primary School
12. Construction of Multipurpose Hall at Langching Sec. School

Proposed Outcome of the project:-


- o Establishment of infrastructure development in the district.


Beneficiaries

- o The project will benefit the population in and around the Chandel district

Observation mentioned in inspection report:

- The project was implemented in 20 locations in in Chandel District, Manipur.
- A total of 12 Components/ Construction scattered in 20 location was approved by NEC under the Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur. Out of which 16 components/project site were inspected. 4 (four) of the project site could not be inspected, 2(two) site due to inaccessible road condition and the other 2(two) as the work has not yet started.


Liza R. Welch
Consultant NE
NEC, Seeth



Anshu Khysim Majat
Consultant (CE)
NEC, Seeth


- Based on the observations found at 16 location inspected, it can be said that the physical progress seems to commensurate with the financial progress.
- **Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong (91.22 sqm)**
 - The works for the Teacher's Transit Quarter at SDO Office Complex, Chakpikarong is seen to be in progress , till date the progress of the construction works at site is 95 %. Earthwork, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
 - Brickworks, plastering works, woodworks, steelworks, installation of windows, doors has been done at site.
 - Finishing works like, painting works, flooring works is seen to be in progress.
 - Internal electrification works has been done at site.
 - Sanitary works, Water closet, HCl soil, waste and vent pipes , is left to be completed.
 - The plinth area i.e 91.22 sqm was found to be more or less as per specification mentioned in the approved DPR.
- **Construction of Teacher's Quarter at Sajik Tampak High School, Manipur. (77.69 sqm)**
 - The works for the Teacher's Quarter at Sajik Tampak High School, Manipur is seen to be in progress, till date the progress of the construction works at site is 80 %. Earthwork, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage.
 - Formworks, Brickworks, plastering has been done at site.
 - Woodworks, steel works for doors and windows, plastering works, installation of windows, doors has not yet started.
 - Finishing works like plastering works, painting works is yet to start.
 - Sanitary works, internal electrification works is yet to start.
 - The plinth area was measured to be around 86.50 sqm which is more than the plinth area i.e 77.69 sqm as per specification mentioned in the approved DPR.
- **Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur. (77.69 sqm)**
 - The works for the Transit Quarter for Doctors' and Nurses at Phoikon, Manipur is seen to be in progress, till date the progress of the construction works at site is 75 %. Earthwork, structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage.
 - Formworks, Brickworks, plastering has been done at site.
 - Woodworks, steel works for doors and windows, plastering works, installation of windows, doors has not yet started.
 - Flooring works is seen to be in progress.
 - Finishing works like plastering works, painting works is yet to start.

Liza R. Heh
Consultant (MB)
1/20. C. H


A. Umjat
Asst. Khayrie Umjat
Consultant (CCB)
NEC, Seft


- Sanitary works, internal electrification works is yet to start.
- The plinth area was measured to be around 87.00 sqm which is more than the plinth area i.e 77.69 sqm as per specification mentioned in the approved DPR.
- **Construction of Primary School at Sugnu Tribal, Manipur. (217.68 sqm)**
 - The works for the Primary School at Sugnu Tribal, Manipur, has been completed, till date the progress of the works at site is 100 %. Earthwork , structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage ..
 - Brickworks, plastering works, woodworks for installation of windows, doors has been done at site.
 - Steel works, roofing and ceiling works has been done at site.
 - Finishing works like painting works, sanitary works, electrification works has been completed.
 - The plinth area for the Primary School at Sugnu Tribal had to be reduced from **217.68 sqm (plinth area in the approved DPR) to 122.63 Sqm**. The implementing department informed that the reduction in the plinth area was due to the need of a toilet as there was no provision of toilet for the school. Extra works like construction of **toilet with plinth area 6.80 sqm and water tank** for the toilet has been carried out and completed.
 - Sanitary works, internal electrification works is yet to start.
- **Construction of Multipurpose Hall at Langching Sec. School, Manipur. (243.92 sqm)**
 - The works for Multipurpose Hall at Langching Sec. School, Manipur, is seen to be in progress, till date the progress of the works at site is 80 %. Earthwork , structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
 - Brickworks, woodworks for installation of windows, doors has been done at site.
 - Steel works, roofing and ceiling works has been completed.
 - Flooring works is seen to be in progress, Plastering works, finishing works and other miscellaneous works the implementing department informed that the work will be completed once the structural works is completed.
 - Remaining finishing works like painting works, electrification works, and other miscellaneous, the implementing agency verbally informed that the remaining works will be started as soon as the structure is complete.
 - The plinth area i.e 243.92 sqm was found to be as per specification mentioned in the approved DPR.


 Liza R. Heh
 Consultant (ME)
 NEC, Sec 4T


 Aarti Khennungat
 Consultant (CE)
 NEC, Sec 4T

- There is a slight change in the orientation of the main door from centre as per the plan to the left corner as per requirements as informed by the implementing department.
- Extra work like provision of a stage was constructed inside the hall as per requirements and need.
- **Water supply scheme at T Phailen, Manipur (27.00 sqm)**
 - The works for Water supply scheme at T Phailen, is seen to be completed, , the percentage progress of the works at site could not be determined although the work was completed as the construction of some of the components is not as per the approved DPR, Earthwork ,structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
 - Brickworks, plastering works, formwork has been done at site.
 - Vertical wall works, Roofing /ceiling works has been completed.
 - The plinth area for the Water supply scheme is measured to be around 14.00 sqm which is very less as compared to the plinth area mentioned in the approved drawing in the approved DPR i.e 27.00 sqm.
- **Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur (111.63 sqm)**
 - The works for Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur, is seen to be in progress, the percentage progress of the works at site is 97%. Earthwork ,structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
 - Brickworks, plastering works, woodworks for installation of windows, doors has been done at site.
 - Steel works, roofing and ceiling works has been done at site.
 - Finishing works like painting works, sanitary works, electrification works is almost completed.
 - Due to site restrictions the plinth area for the Classrooms had to be reduced from 111.63 sqm (plinth area in the approved DPR) to 90.00 sqm and accordingly there is a reduction of 2 nos of column from the original plan of the School, which is compensated with the additional construction of verandah and ramp of plinth area 18.11 sqm having 4 circular pillar has been carried out at the Kovol primary school with the total plinth area coming up to 108.11 sqm.
- **Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur (212.46 Rm)**
 - The works for barb wire fencing with gate at Khubung Khunou Primary School, Manipur, is seen to be completed, the percentage progress of the works at site is 100%.
 - Earthwork ,formwork in foundation, footings, bases of columns, structural details such as Reinforcement details and concrete mix


 Liza R. Hale
 Consultant (NE)
 NEC, Guwahati


 A. M. Rajat
 Consultant (NE)
 NEC, Guwahati

- design etc could not be checked as works has been done at the initial stage .
- Approximately 230 Rm of barb wire fencing with gate has been constructed which is more than the length given in the approved DPR i.e 212.46 Rm
 - **Construction of Public Toilet at Chakikarong Bazar, Manipur (6.94 sqm)**
 - The works for Construction of Public Toilet at Chakikarong Bazar, Manipur, is seen to be in progress, the percentage progress of the works at site could not be determined as the construction of some of the components is not as per the approved DPR.
 - Earthwork ,structural details such as Reinforcement details and concrete mix design etc could not be checked as works has been done at the initial stage .
 - Brickworks, plastering works, woodworks for installation of windows, doors has been done at site.
 - Steel works, roofing and ceiling works has been done at site.
 - Finishing works like painting works, sanitary works, electrification works is almost completed.
 - No separate provision for Urinal was found at site, instead the urinal was found to be constructed in one of the toilets with no such partition or wall in between.
 - The plinth area i.e 6.94 sqm was found to be more or less as per specification mentioned in the approved DPR.
 - **Installation of borewell at 9 locations @ 4 lakhs per unit, Manipur.**
 - The works for Installation of borewell at 9 locations, is seen to be in progress, the percentage progress of the works at site is around 78%.
 - Installation of borewell is completed at 7 locations and it is found to be functional and catering to the need of the people in the area. For the remaining 2(two) installation work has not yet started.
 - Regarding aims and objective we can say that somehow the project was able to cater the need of the people in the village of Chandel District.the project which is committed to raising the living standards of its citizens and ensuring inclusive growth for all – “Sabka Saath Sabka Vikas aur Sabka Vishwas”. While interacting with the villagers they express gratitude, for example the installation of borewell has helped them tremendously. As water management and services, Infrastructure is absolutely essential for eradication of poverty and is necessary condition for enabling sustained economic growth
 - A signboard acknowledging NEC funding was not found at all the sites. Therefore, the Implementing Department was asked to erect a permanent signboard stating that the project was funded by NEC


Liza . R. Heli
Consultant (HE)
NEC, Sectt


Anshu Khysimrajat
Consultant (CE)
NEC, Sectt

Report of the inspection carried on 22/06/2022 for the NEC funded project "Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur".


A joint inspection of the above project was carried out by the officials of NEC Secretariat, Shillong and officials of District Rural Development Agency, Govt. of Manipur on 22/06/2022. The list of the officials present during the inspection is enclosed as Annexure-I & The photographs taken during the time of inspection is enclosed as Annexure-II.


1) Background:

Name of the project	Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur
Location	Chandel District, Manipur
Implementing Department	District Rural Development Agency, Deputy Commissioner, Chandel district, Govt. of Manipur
Date of Approval	21-10-2020
Date of Sanction	21-10-2020
Cost of the project	286.00 Lakh
NEC Share (100%)	286.00 Lakh
NEC Share released & Date	Rs. 114.00 Lakh on 21-10-2020
Total amount released	Rs. 114.00 Lakh
Balance amount to be released by NEC	Rs. 172.00 Lakh
State Share Released	NA
Balance amount to be released by the State Govt.	NA
Status of UC for NEC share	Rs. 114.00 Lakh
Target Date of Completion	21-10-2022
Time Overrun	NA

II) Aims/ Objective of the Project

- a) Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur is to provide accommodation facility for Doctors and Nurses at PHC Sajik Tampak.
- b) Water supply scheme at T Phailen, Manipur is to provide tapped drinking water to at least 50 households in and around T Phailen Village.
- c) Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur is to provide secure existing primary school with aim to consolidate the existing infrastructure.
- d) Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong, Manipur is to provide transit accommodation facility to Government Teachers in and around Chakpikarong Sub-Division Hqtr. Area.


Liza R. Hall
Consultant (NEC)
NEC Secret


Aarti Khayiemuijat
Consultant (CCED)
NEC, Seeth.

- e) Construction of Primary School at Sugnu Tribal, Manipur is to provide primary education at Sugnu Tribal area.
- f) Construction of Doctors' and Nurse Transit Quarter at PHSC Khubung Khullen, Manipur is to provide accommodation facility for Doctors and Nurses of PHSC Khubung Kullen.
- g) Construction of 2 additional Classrooms at Kovol Primary School, Tami, Chandel district is to provide additional classrooms to accommodate at least 40 more students.
- h) Installation of borewell at 9 locations/ village, Manipur is to provide tapped drinking water to water deficient villages.
- i) Construction of Public Toilet at Chakikarong Bazar, Manipur is to provide clean and improved sanitation facility at Chakpikarong Hqtr. Bazaar.
- j) Construction of Teacher's Quarter at Sajik Tampak High School, Manipur is to provide accommodation facility for teachers of Sajik Tampak High School, Sajik Tampak.
- k) Construction of 2 additional Class rooms at Phiram Mchet Primary School, Manipur is to provide additional classrooms to accommodate at least 30-40 students.
- l) Construction of Multipurpose Hall at Langching Sec. School, Manipur is to provide educational and recreational activities of Langching primary and secondary schools.


(III) Observations/ Status of works (Physical Achievements):


Sl. No	Approved items of Works	Approved Cost (Rs. In Lakhs)	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
1	Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong	29.75	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Cement Concrete works in foundation and plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, beam, lintel and slab has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided • Reinforced Cement Concrete Work in substructure, columns, pillars, roofs, landing beams upto slab level, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks have been completed. • Brick work, Plastering works, Wood work, Ceiling works, Roofing works, Steel works has been completed. • Doors and windows has been fixed. 	<ul style="list-style-type: none"> • Flooring, finishing/painting works is seen to be in progress. • Water closet, HCl soil, waste and vent pipes is left to be completed. 	• NIL

*Liza R. Nakh
Consultant HCE
11*


*A. K. Singh
Asstt. Engineer
Consultant CCEV
NGC, Sectt.*


2	Construction of Teacher's Quarter at Sajik Tampak High School, Manipur.	21.81	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Plain cement Concrete works in foundation and plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, beam, lintel and slab has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided • Reinforced Cement Concrete Work in substructure, columns, pillars, roofs, landing beams upto slab level, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks have been completed. • Floor casting work has been completed. • Brick work, Ceiling/roofing works has been completed. 	<ul style="list-style-type: none"> • Plastering works • Wood work on doors and windows • Steel works for doors and windows. • Finishing/painting works. • Sanitary works, internal electrification works 	• NIL
3	Construction of Doctors' and Nurse Transit Quarter at PHSC Khubung Khullen, Manipur	21.81	<ul style="list-style-type: none"> • This project site could not be inspected due to inaccessible road condition because of bad weather (heavy rainfalls), the implementing department informed that some of the sites can only be visited during dry weather seasons possibly in the month of November. 	• NA	• NA
4	Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur.	21.81	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Plain cement Concrete works in foundation and plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, beam, lintel and slab has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided • Reinforced Cement Concrete Work in substructure, columns, pillars, roofs, landing beams upto slab level, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks have been completed. • Brick work, Ceiling/roofing works has been completed. 	<ul style="list-style-type: none"> • Flooring works. • Plastering works • Wood work on doors and windows • Steel works for doors and windows. • Finishing/painting works. • Sanitary works, internal electrification works 	• NIL


Liza. R. Heh
Consultant (M.E.)
11/11/2023



A. Sujat
Consultant (M.E.)
NEC, Seeth.


5	Construction of Primary School at Sugnu Tribal, Manipur.	27.10	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Cement Concrete works in foundation upto plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided • Reinforced Cement Concrete Work in substructure, columns, pillars, floor beams, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks have been completed. • Floor casting work has been completed. • Brick work, Plastering works, Wood work, Ceiling works, Roofing works, Steel works has been completed. • Finishing/painting works has also been completed. 	• NIL	<ul style="list-style-type: none"> • During inspection the plinth area was measured to be around 122.63 Sqm which is lesser than the plinth area mentioned in the approved DPR (i.e 217.68 Sqm). • The implementing department informed that the reduction in the plinth area was due to the need of a toilet as there was no provision of toilet for the school. • Extra works like construction of toilet of plinth area 6.80 Sqm and water tank for the toilet has been carried out and completed.
---	--	-------	--	-------	--


 Liza R. Heli
 Consultant (ME)
 NEC, Sealt


 Aarti Khysimmyat
 Consultant CCE
 NEC, Sealt

6	Construction of Multipurpose Hall at Langching Sec. School, Manipur.	24.69	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Cement Concrete works in foundation and plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, beam, lintel and slab has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided. • Reinforced Cement Concrete Work in substructure, columns, pillars, roofs, landing beams upto slab level, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks have been completed. • Brick work, Plastering works, Wood work, Ceiling works, Roofing works, Steel works has been completed. • Doors and windows has been fixed. 	<ul style="list-style-type: none"> • Finishing/painting works is seen to be in progress. • Internal electrification works. 	<ul style="list-style-type: none"> • Orientation of the main door changed from centre to the left corner as per requirements as informed by the implementing department. • A stage was constructed inside the hall as per requirements and needs.
7	Water supply scheme at T Phailen, Manipur	15.73	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Plain cement Concrete works in foundation and plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation upto plinth level, has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided • Reinforced Cement Concrete Work in substructure upto plinth columns, pillars, has been completed, so the consultants could not give any comments regarding the design mix. • Formwork, vertical walls works, flooring works, plinth protection works has been completed. 	• NIL	<ul style="list-style-type: none"> • The plinth area for the Water supply scheme is measured to be around 14.00 sqm which is very less as compared to the plinth area mentioned in the approved drawing in the approved DPR i.e 27.00 sqm


Liza R. Hek
Consultant (ME)
NEC, Seelt



Aniti Khysimoujat -
Consultant (CE)
NEC, Seelt


8	Construction of 2 additional Class rooms at Phiram Machet Primary School, Manipur.	12.04	<ul style="list-style-type: none"> • This project site could not be inspected due to inaccessible road condition because of bad weather (heavy rainfalls), the implementing department informed that some of the sites can only be visited during dry weather seasons possibly in the month of November. 	• NA	• NA
9	Construction of 2 additional Classrooms at Kovol Primary School, Tami	12.04	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Cement Concrete works in foundation upto plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided • Reinforced Cement Concrete Work in substructure, columns, pillars, floor beams, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks have been completed. • Floor casting work has been completed. • Brick work, Plastering works, Wood work, Ceiling works, Roofing works, Steel works has been completed. 	• Finishing/painting works is left to be completed.	<ul style="list-style-type: none"> • During inspection the plinth area was measured to be around 90 Sqm which is lesser than the plinth area mentioned in the approved DPR (i.e 111.63 Sqm) and accordingly there is a reduction of 2 nos of column from the original plan of the School. • During inspection it was observed that an additional construction of verandah and ramp of plinth area 18.11 sqm having 4 circular pillar has been carried out at the Kovol primary school.

*Lizer R. Heli
 Consultant (ME)
 NEC, Seclt*

*A. Mujat
 Aarti Khyrie m. mujat
 Consultant (CE)
 NEC, Seclt.*

10	Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur	12.94	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Cement Concrete works in foundation upto plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided. • Reinforced Cement Concrete Work in substructure, columns, pillars, floor beams, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks, steelworks have been completed. • Floor casting work has been completed. • Brick work, Plastering works, Wood work, Ceiling works, Roofing works, Steel works has been completed 	• NIL	<ul style="list-style-type: none"> • Approximately 230 Rm of barb wire fencing has been constructed which is more than the length given in the approved DPR i.e 208.08 Rm.
11	Construction of Public Toilet at Chakikarong Bazar, Manipur	2.97	<ul style="list-style-type: none"> • Works related to earthwork, stone soling works, has been done at the initial stage. • Cement Concrete works in foundation upto plinth has been completed so the inspection team could not give any comments. • Steel Reinforcement for foundation column, plinth beam, has been completed so the consultant cannot give any comments regarding the no. and size of reinforcement provided • Reinforced Cement Concrete Work in substructure, columns, pillars, floor beams, has been completed, so the consultants could not give any comments regarding the design mix. • Formworks have been completed. • Floor casting work has been completed. • Brick work, Plastering works, Wood work, Ceiling works, Roofing works, Steel works has been completed. 	• NIL	<ul style="list-style-type: none"> • During inspection it was found out that no separate urinal was constructed, the urinal was constructed inside one of the toilet.


 Liza R. Heh
 Consultant (ME)
 NEC, Sectt


 Anis Khayimujat
 Consultant (CE)
 NEC, Sectt

12.	Installation of borewell at 9 locations @ 4 lakhs per unit, Manipur	30.96	• Installation of borewell at 7 locations completed i.e	• Installation of borewell at 2 locations i.e is left to be done.	• NIL
	Total	23365000.00			
	Add 10% IEI (Sl. No. 1-6)	1469700.00			
	Add 12% GST	2803800.00			
	Add 1% Cess LWF	233650.00			
	Add 3% Contingency charge	700950.00			
	Grand Total	28573100.00			
	Grand Total (Say)	286.00 Lakhs			

(IV) Location Of The Project:

Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong	Latitude: 24. 206634° N Longitude: 93.904557° E
Construction of Teacher's Quarter at Sajik Tampak High School, Manipur.	Latitude: 24. 08316° N Longitude: 93.50368 ° E
Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur.	Latitude: 24. 07926° N Longitude: 93.50259 ° E
Construction of Primary School at Sugnu Tribal, Manipur.	Latitude: 24. 17661° N Longitude: 93.52693 ° E
Construction of Multipurpose Hall at Langching Sec. School, Manipur.	Latitude: 24. 18133° N Longitude: 93.52616° E
Water supply scheme at T Phailen, Manipur	Latitude: 24. 08338° N Longitude: 93.50656° E

[Handwritten Signature]
Liza. R. H. Chell
Consultant (P&I)

[Handwritten Signature]
Aarti Khosla
Consultant (C&E)
N.P.C. Co. Ltd.

Construction of 2 additional Classrooms at Kovol Primary School, Tami	Latitude: 24. 208568° N Longitude: 93.897895 ° E
Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur	Latitude: 24. 200622° N Longitude: 93.904559° E
Construction of Public Toilet at Chakikarong Bazar, Manipur	Latitude: 24. 205909° N Longitude: 93.90318° E
Installation of borewell at 9 locations @ 4 lakhs per unit, Manipur	
B. JANGNOUPHAI VILLAGE-	Latitude: 24. 294998° N Longitude: 93.881839° E
UTANGPOKPIVILLAGE-	Latitude: 24. 16628° N Longitude: 93.53100° E
Y. KHUTHAVILLAGE-	Latitude: 24. 210881° N Longitude: 93.911732° E
SENGUL COLONYVILLAGE-	Latitude: 24. 206177° N Longitude: 93.910872° E
KHUSI TAMPAKVILLAGE-	Latitude: 24. 205314° N Longitude: 93.911255° E
BEAULAVILLAGE-	Latitude: 24. 193153° N Longitude: 93.902541° E
THUNGCHENG VILLAGE-	Latitude: 24. 290013° N Longitude: 93.899085° E

(V) Overall Remarks and Suggestions:

During inspection the following observations were made:

- **The Project is for Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur.**
- The project was implemented in 20 locations in in Chandel District, Manipur.
- A total of 12 Components/ Construction scattered in 20 location was approved by NEC under the Development Programme of Identified Backward Block Under 30% Central Sector Scheme of NEC in Chandel District, Manipur. Out of which 16 components/project site were

[Signature]
Liza. R. Heli
Consultant (ME)
NEC, Sect

[Signature]
A. M. Mijet
Consultant (CE)
NEC, Sect

- inspected.** 4 (four) of the project site could not be inspected, 2(two) site due to inaccessible road condition and the other 2(two) as the work has not yet started.
- Based on the observations found at 16 location inspected, it can be said that the physical progress seems to commensurate with the financial progress.
 - **(i) Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong (91.22 sqm)**
 - The works for the **Teacher's Transit Quarter at SDO Office Complex, Chakpikarong** is seen to be in progress , till date the progress of the construction works at site is **95 %**. Earthwork, structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage .
 - **Brickworks**, plastering works, woodworks, steelworks, installation of windows, doors has been **done** at site.
 - **Finishing** works like, painting works, flooring works is seen to be in progress.
 - Internal electrification works has been done at site.
 - Sanitary works, Water closet, HCl soil, waste and vent pipes , is left to be completed.
 - The plinth area i.e **91.22 sqm** was found to be more or less **as per specification** mentioned in the approved DPR.
 - A **signboard** acknowledging NEC funding was **not found** at site.
 - **(ii) Construction of Teacher's Quarter at Sajik Tampak High School, Manipur. (77.69 sqm)**
 - The works for the **Teacher's Quarter at Sajik Tampak High School, Manipur** is seen to be in progress, till date the progress of the construction works at site is **80 %**. Earthwork, structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage.
 - **Formworks, Brickworks**, plastering has been **done** at site.
 - Woodworks, steel works for doors and windows, plastering works, installation of windows, doors has not yet started.
 - **Finishing** works like plastering works, painting works is yet to start.
 - Sanitary works, internal electrification works is yet to start.
 - The plinth area was measured to be around **86.50 sqm** which is more than the plinth area i.e **77.69 sqm** as per specification mentioned in the approved DPR.
 - A **signboard** acknowledging NEC funding was **not found** at site
 - **(iii) Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur. (77.69 sqm)**
 - The works for the **Transit Quarter for Doctors' and Nurses at Phoikon, Manipur** is seen to be in progress, till date the progress of the construction works at site is **75 %**. Earthwork, structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage.
 - **Formworks, Brickworks**, plastering has been **done** at site.
 - Woodworks, steel works for doors and windows, plastering works, installation of windows, doors has not yet started.
 - Flooring works is seen to be in progress.
 - **Finishing** works like plastering works, painting works is yet to start.

[Signature]
 Liza R. Heli
 Consultant
 11/11/11


[Signature]
 Aarti Khayemrajat
 Consultant
 NEC, Scott


- Sanitary works, internal electrification works is yet to start.
- The plinth area was measured to be around **87.00 sqm** which is more than the plinth area i.e **77.69 sqm** as per specification mentioned in the approved DPR.
- A **signboard** acknowledging NEC funding was **not found** at site
- **(iv) Construction of Primary School at Sugnu Tribal, Manipur. (217.68 sqm)**
 - The works for the **Primary School at Sugnu Tribal, Manipur**, has been completed, till date the progress of the works at site is **100 %**. Earthwork , structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage ..
 - **Brickworks**, plastering works, woodworks for installation of windows, doors has been **done** at site.
 - **Steel works, roofing and ceiling works** has been **done** at site.
 - **Finishing** works like painting works, sanitary works, electrification works has been completed.
 - The plinth area for the **Primary School at Sugnu Tribal** had to be reduced from **217.68 sqm** (plinth area in the approved DPR) to **122.63 Sqm**. The implementing department informed that the reduction in the plinth area was due to the need of a toilet as there was no provision of toilet for the school. Extra works like construction of toilet of plinth area **6.8 sqm** and water tank for the toilet has been carried out and completed.
 - Sanitary works, internal electrification works is yet to start.
 - A **signboard** acknowledging NEC funding was **found** at site.
- **(v) Construction of Multipurpose Hall at Langching Sec. School, Manipur. (243.92 sqm)**
 - The works for **Multipurpose Hall at Langching Sec. School, Manipur**, is seen to be in progress, till date the progress of the works at site is **80 %**. Earthwork, structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage .
 - **Brickworks**, woodworks for installation of windows, doors has been **done** at site.
 - **Steel works**, roofing and ceiling works has been **completed**.
 - **Flooring works** is seen to be in progress, Plastering works, finishing works and other miscellaneous works the implementing department informed that the work will be completed once the structural works is completed.
 - Remaining **finishing** works like painting works, electrification works, and other miscellaneous, the implementing agency verbally informed that the remaining works will be started as soon as the structure is complete.
 - The plinth area i.e **243.92 sqm** was found to be **as per specification** mentioned in the approved DPR.
 - There is a slight change in the orientation of the main door from centre as per the plan to the left corner as per requirements as informed by the implementing department.
 - Extra work like provision of a stage was constructed inside the hall as per requirements and need.
 - A **signboard** acknowledging NEC funding was **not found** at site
- **(vi) Water supply scheme at T Phailen, Manipur (27.00 sqm)**

[Signature]
 Liza . R. Ithah
 Consultant (ME)
 NEC, S & IT

[Signature]
 Aarti Khayriemujat
 Consultant (CE)
 NEC, S&IT

- The works for **Water supply scheme at T Phailen**, is seen to be completed, , the percentage progress of the works at site could not be determined although the work was completed as the construction of some of the components is not as per the approved DPR, Earthwork ,structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage .
- **Brickworks**, plastering works, formwork has been **done** at site.
- Vertical wall works, Roofing /ceiling works has been **completed**.
- The plinth area for the **Water supply scheme** is measured to be around **14.00 sqm** which is very less as compared to the plinth area mentioned in the approved drawing in the approved DPR i.e **27.00 sqm**.
- A **signboard** acknowledging NEC funding was **not found** at site
- **(vii) Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur (111.63 sqm)**
 - The works for **Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur**, is seen to be in progress, the percentage progress of the works at site is 97%. Earthwork ,structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage .
 - **Brickworks**, plastering works, woodworks for installation of windows, doors has been **done** at site.
 - **Steel works, roofing and ceiling works** has been **done** at site.
 - **Finishing** works like painting works, sanitary works, electrification works is almost completed.
 - Due to site restrictions the plinth area for the **Classrooms** had to be reduced from **111.63 sqm** (plinth area in the approved DPR) to **90.00 sqm** and accordingly there is a reduction of 2 nos of column from the original plan of the School, which is compensated with the additional construction of verandah and ramp of plinth area 18.11 sqm having 4 circular pillar has been carried out at the Kovol primary school with the total plinth area coming up to **108.11 sqm**.
 - A **signboard** acknowledging NEC funding was **found** at site
- **(viii) Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur (212.46 Rm)**
 - The works for **barb wire fencing with gate at Khubung Khunou Primary School, Manipur**, is seen to be completed, the percentage progress of the works at site is 100%.
 - Earthwork ,formwork in foundation, footings, bases of columns, structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage .
 - Approximately **230 Rm** of barb wire fencing **with gate** has been constructed which is **more** than the length given in the approved DPR i.e 212.46 Rm.
 - A **signboard** acknowledging NEC funding was **found** at site
- **(ix) Construction of Public Toilet at Chakikarong Bazar, Manipur (6.94 sqm)**
 - The works for **Construction of Public Toilet at Chakikarong Bazar, Manipur**, is seen to be in progress, the percentage progress of the works at site could not be determined as the construction of some of the components is not as per the approved DPR.


Liza R. Nel
Consultant (E.E.)
NEC, Sectt


A. unjat
Consultant CCEX
NEC, Sectt


- Earthwork ,structural details such as Reinforcement details and concrete mix design etc **could not be checked** as works has been done at the initial stage .
- **Brickworks**, plastering works, woodworks for installation of windows, doors has been **done** at site.
- **Steel works, roofing and ceiling works** has been **done** at site.
- **Finishing** works like painting works, sanitary works, electrification works is almost completed.
- No separate provision for Urinal was found at site, instead the urinal was found to be constructed in one of the toilets with no such partition or wall in between.
- The plinth area i.e **6.94 sqm** was found to be more or less **as per specification** mentioned in the approved DPR.
- A **signboard** acknowledging NEC funding was **found** at site
- **(x) Installation of borewell at 9 locations @ 4 lakhs per unit, Manipur.**
 - The **works for Installation of borewell at 9 locations**, is seen to be in progress, the percentage progress of the works at site is around 78%.
 - Installation of borewell is completed at 7 locations and it is found to be functional and catering to the need of the people in the area. For the remaining 2(two) installation work has not yet started.
 - A **signboard** acknowledging NEC funding was **found** at site
- Regarding aims and objective we can say that somehow the project was able to cater the need of the people in the village of Chandel District. the project which is committed to raising the living standards of its citizens and ensuring inclusive growth for all – “**Sabka Saath Sabka Vikas aur Sabka Vishwas**”. While interacting with the villagers they express gratitude, for example the installation of borewell has help them tremendously. As water management and services, infrastructure is absolutely essential for eradication of poverty and is necessary condition for enabling sustained economic growth.


Proposed Outcome of the project:- .

- o Establishment of infrastructure development in the district.

Beneficiaries

- o The project will benefit the population in and around the Chandel district






 Liza R. Hill
 Consultant (ME)
 NEC, Sectt.


 Anis Khyrie Masujat
 Consultant CCE
 NEC, Sectt.




List of officials who were present during the inspection of NEC funded project
 "Development Programme of Identified Backward Block Under 30 PC Central Sector
 Scheme of NEC in Chandel District, Manipur" on 22.1.2022


Sl. No	Name	Contact No. & Email id	Designation & Organisation/Department	Signature
1.	Melody	7005016610	Chief I/c, Sugra	Melody.
2.	Seiminhan Bate	7085348645	Chief.	Seiminhan.
3.	Sethulal	9615352435	Chief	Sethulal.
4.	Thangphomang Bate	9612200694	Chief, itang pokpi	Thangphomang.
5.	Sebastian	8415032139	Chief Tampi	Sebastian.
6.	Hutan Changking	8837214809	President B.T.P 41 Chandel	Hutan Changking.
7.	Parshaband Anal	8416052593	Chief y. khuthe village	Parshaband.
8.	Foyse Sengul	7005245744	Chief Sengul Colony	Foyse Sengul.
9.	Hutan Changking	8837214809	President B.T.P 41 Chandel	Hutan Changking.
10.	Sng. Benjamin	9366831833	Chief Chubung Khemas village.	Sng. Benjamin.
11.	S. y. Man	8731960444 6761460444	Chief Beula	S. y. Man.
12.	Mohd. Afjal Khan	7005646554	T.A. / PRO / EDL	Mohd. Afjal Khan.

List of officials who were present during the inspection of NEC funded project
 "Development Programme of Identified Backward Block Under 30 PC Central Sector
 Scheme of NEC in Chandel District, Manipur" on 22/06/2022

Sl. No	Name	Contact No. & Email id	Designation & Organisation/Department	Signature
13	SE AOC/imp	9005821038	T A / C / S	
214	H. Shanta S.	841395305	A.E.-IDRPA/ CHANDEL	
315	H. Singh	600215 9511	A&P/imp.	
4.16	Aarti Khyismunyat	8979593379	Consultant (C), NEC	
5.				
6.				
7.				
8.				
9.				
10.				
11.				
12.				

List of officials who were present during the inspection of NEC funded project
**"Development Programme of Identified Backward Block Under 30 PC Central Sector
 Scheme of NEC in Chandel District, Manipur" on 22./06./2022**

Sl. No	Name	Contact No. & Email id	Designation & Organisation/Department	Signature
1.	Th. Ajit Singh.	7085611365 thajitha@ gmail.com	Section Officer	
2.	L. Milajit Singh	9426035360 Milajitlong@ gmail.com	EE	
3.	Kiza. R. Heh	9774335292	Consultant ME	
4.				
5.				
6.				
7.				
8.				
9.				
10.				
11.				
12.				

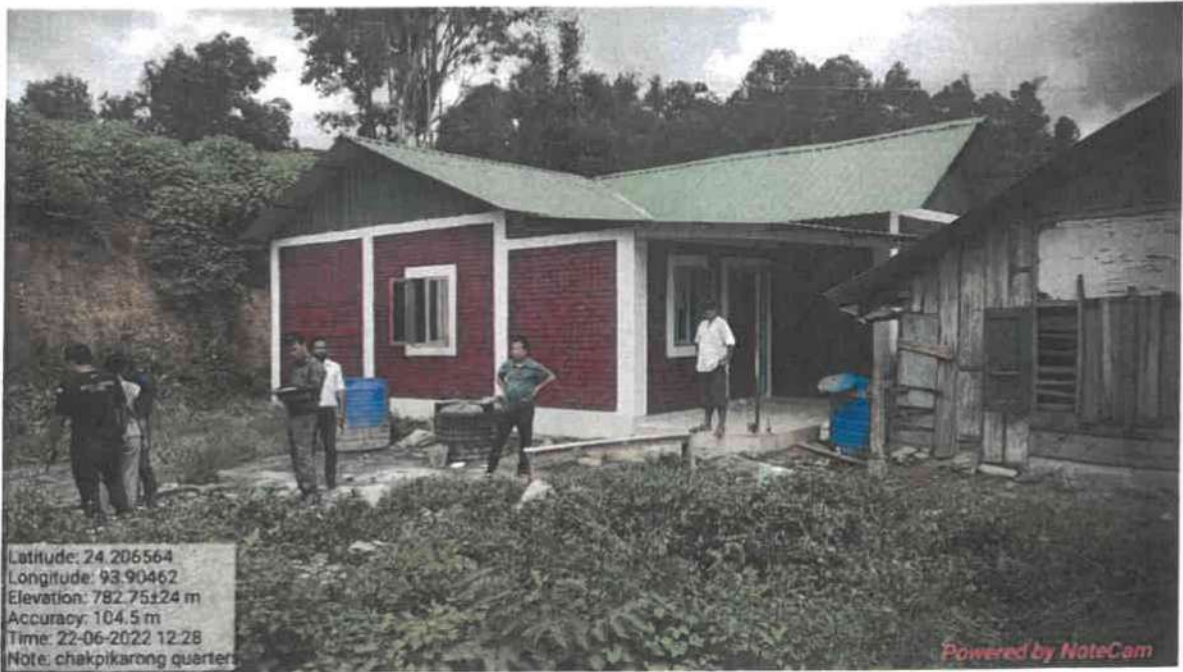

Overall view of the "Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong"



Front view of the "Construction of Teacher's Transit Quarter at SDO Office Complex, Chakpikarong"

[Signature]
 Liza. R. Heli
 Consultant (ME)
 NEC, Sectr


[Signature]
 Aarti Khyiemnujat
 Consultant (CE)
 NEC, Sectt.



View inside the room for “Construction of Teacher’s Transit Quarter at SDO Office Complex, Chakpikarong”



Side view of the “Construction of Teacher’s Transit Quarter at SDO Office Complex, Chakpikarong”


Liza R. Heck
Consultant ME
NEC, Sectt


Aarti Khysicunijat
Consultant CCE
NEC, Sectt.




View inside the toilet of the “Construction of Teacher’s Transit Quarter at SDO Office Complex, Chakpikarong”




Overall view of the “Construction of Primary School at Sugnu Tribal, Manipur”

[Signature]
Lizy R. Huh
Consultant-ME
NEC, Sectt

[Signature]
Aarti Khayierunjat
Consultant (CE)
NEC, Sectt

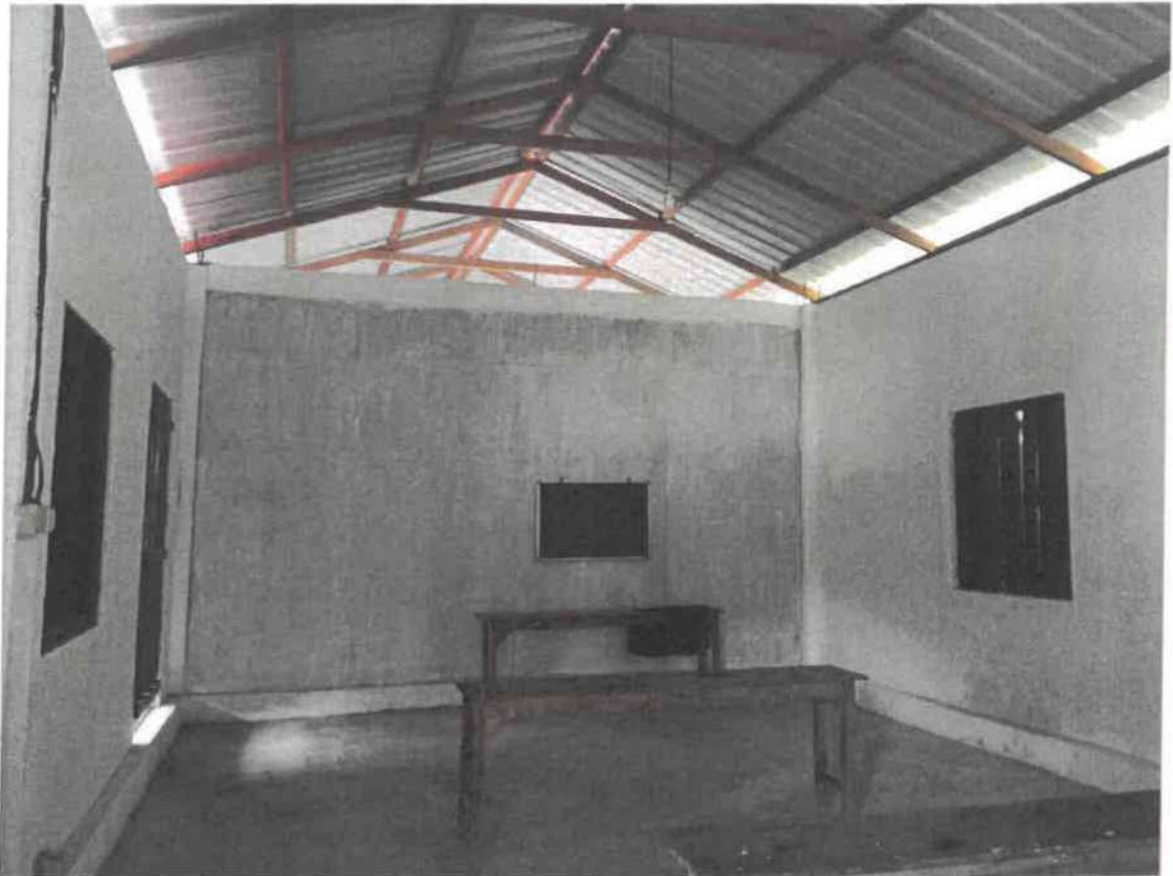

Inside view of the "Construction of Primary School at Sugnu Tribal, Manipur"

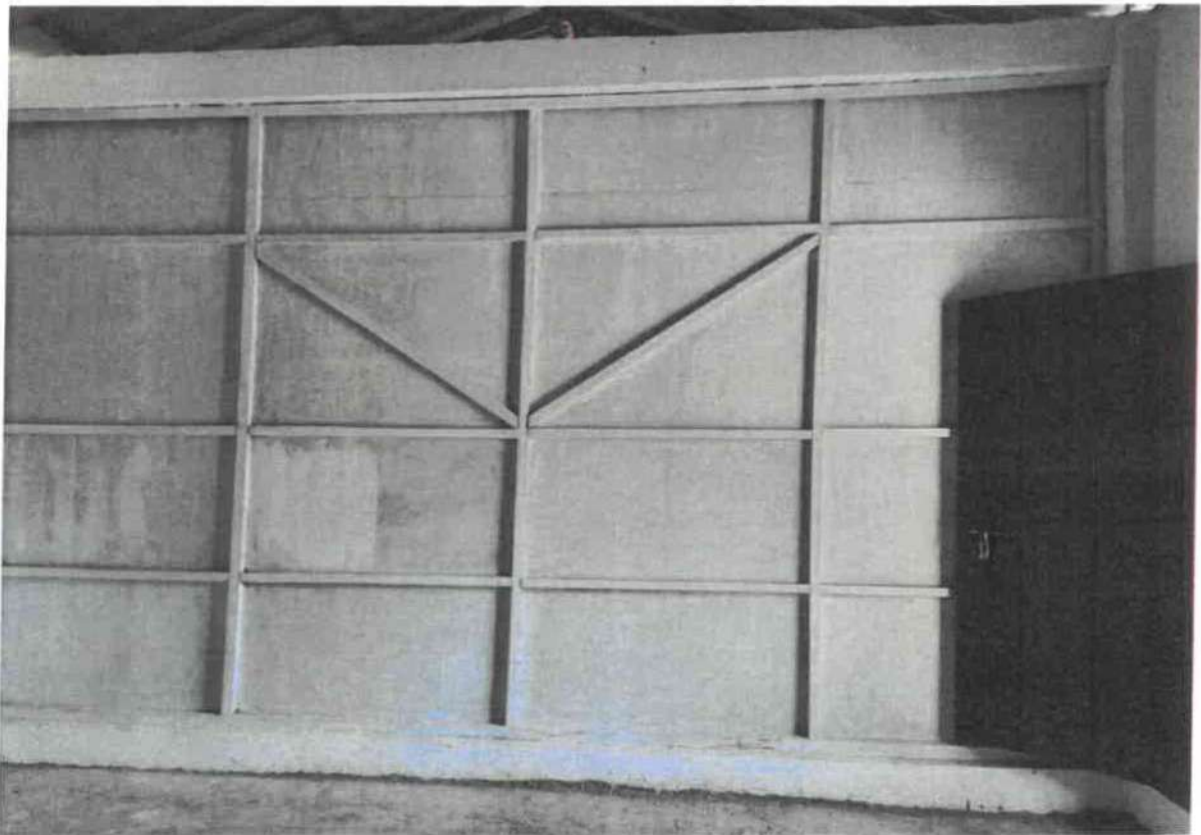

Hard board partition for "Construction of Primary School at Sugnu Tribal, Manipur"

[Signature]
 Liza R. Velh
 Consultant (ME)
 N.E.C. Co. Ltd

[Signature]
 Aarti Khysienmyat
 Consultant CCB
 N.E.C. Sect.



Photo showing the Toilet constructed at "Construction of Primary School at Sugnu Tribal, Manipur"



Overall view of the "Construction of Multipurpose Hall at Langching Sec. School, Manipur".

[Signature]
Liza . R. Hell
Consultant (ME)
NEC, Secht

[Signature]
Aarti Khayiesonmyat
Consultant (CE)
NEC, Secht.



Overall view of the "Construction of Multipurpose Hall at Langching Sec. School, Manipur".



View inside the "Construction of Multipurpose Hall at Langching Sec. School, Manipur".

[Signature]
Liza R. Heli
Consultant (ME)
NEC, Seclt

[Signature]
Aarti Khyiemajet
Consultant (CE)
NEC, Seclt.



Overall view of "Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur"



Inside view showing the doors and windows of "Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur"

Liza R. Helli
 Consultant (ME)
 Nir. S. Lt.

M. Sujat
 Asst. Dy. Comm. Insp.
 Consultant (CB)
 NEC, Smt.



View showing the roofing/ceiling works of "Construction of 2 additional Classrooms at Kovol Primary School, Tami, Manipur"



Photograph of the gate for "Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur"

[Signature]
Liza R. Heh
Consultant (ME)
NEC, Sectt

[Signature]
Aarti Khajimujat
Consultant (CE)
NEC, Sectt.



Photograph showing the barb wire fencing for the “Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur”



Photograph of inspection team at the site “Construction of barb wire fencing with gate at Khubung Khunou Primary School, Manipur”

Liza R. Heh
 Liza R. Heh
 Computer (NE)
 NEC, Sectt

A. Mijet
 Aarti Khysiemijet
 Consultant CCEP
 NEC, Sectt.



Photograph showing the “Construction of Public Toilet at Chakikarong Bazar, Manipur”



Photograph showing the sanitary pipelines for “Construction of Public Toilet at Chakikarong Bazar, Manipur”

[Signature]
 Liza R. Hell
 Consultant-(MO)
 NEG, ICHT

[Signature]
 Aarti Khyrie Majat
 Consultant (CG)
 NEC, Seeth



Photo of the inspection team for “Installation of borewell at B. Jangnoupai Village” – Location 1

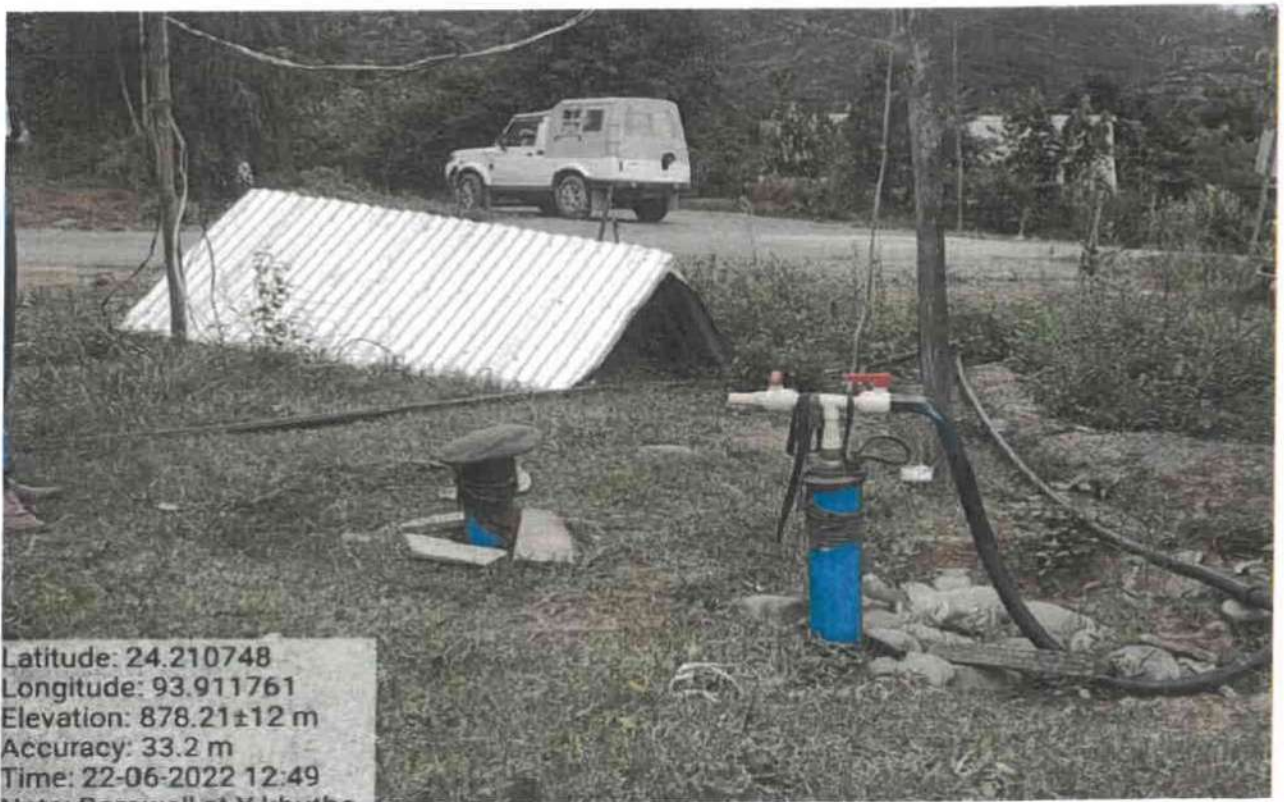


Photo of the “Installation of borewell at Y. Khutha Village” – Location 3

Liza R. Hall
 Consultant (NE)
 NRC, Seattle

Dr. Nijat
 NRC, Seattle
 Consult. (CEV)
 NRC, Seattle



Photo of the "Installation of borewell at Sengul Colony village" – Location 4

[Signature]
 Liza. R. Hall
 Consultant (HE)
 NEC, Sect

[Signature]
 Anis Khayemmyat
 Consultant CCEB
 NEC, Sect



Photo of the borewell and the water tank for the "Installation of borewell at Khusi Tampakvillage" – Location 5

A. Nujat
Nanti Khayiamujat
Consultant (CE)
NEC, Sett.



Latitude: 24.193193
 Longitude: 93.902558
 Elevation: 796.25±16 m
 Accuracy: 5.4 m
 Time: 22-06-2022 13:57
 Note: borewell at Beula



Latitude: 24.193156
 Longitude: 93.902541
 Elevation: 802.54±12 m
 Accuracy: 10.6 m
 Time: 22-06-2022 14:00
 Note: borewell at Beula

Powered by NoteCam

Photo of the "Installation of borewell at Beula village" alongwith the inspection team – Location 6

Liza R. Dell
 Consultant - (MG)
 NRC, Co-IT


Dr. Nijat
 Asst. Physiotherapist
 Consultant (CCB)
 NEC, Sect.




Photo of the “Installation of borewell at Thungcheng village”– Location 7



Photo of the inspection team at “Construction of Teacher’s Quarter at Sajik Tampak High School, Manipur


Liza. R. Hell
Consultant- (ME)
NEC, Sec II



Aniti Khyni Mawjat.
Consultant (CA)
NEC, Sec II.




Photograph showing the "Water supply scheme at T Phailen, Manipur"



Overall view of "Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur."

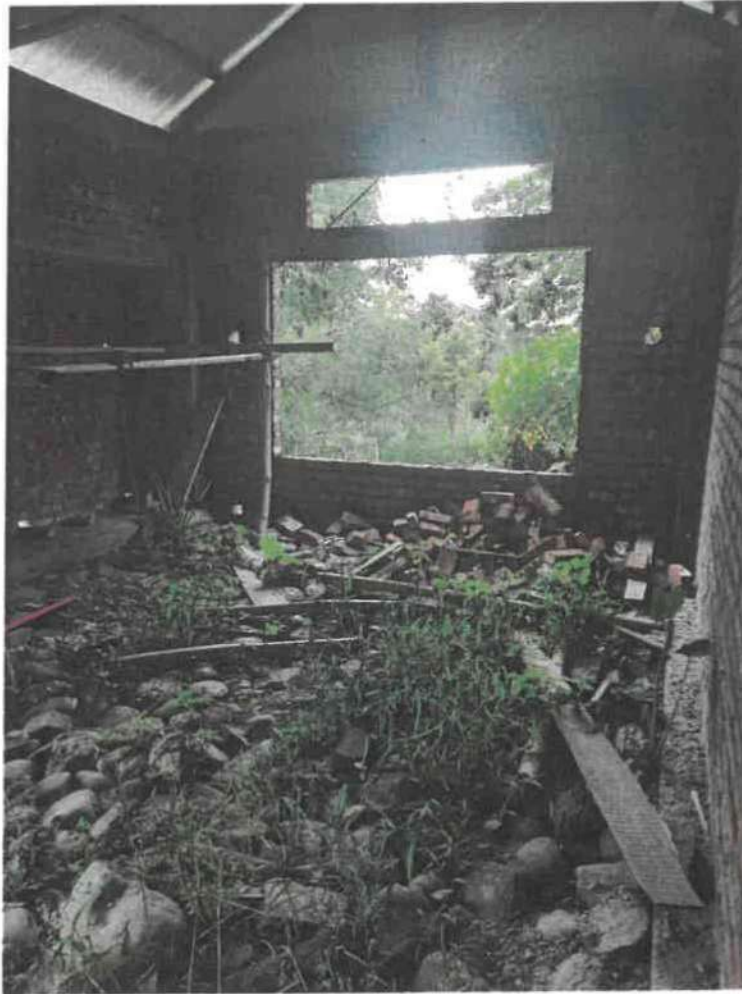

Liza. R. Hek
Consultant - (ME)
NEC, SecIT




Inside view of "Construction of Transit Quarter for Doctors' and Nurses at Phoikon, Manipur."



Overall view of "Construction of Teacher's Quarter at Sajik Tampak High School, Manipur"


Liza. R. Hek
Consultant - (ME)
NEC, Seattle

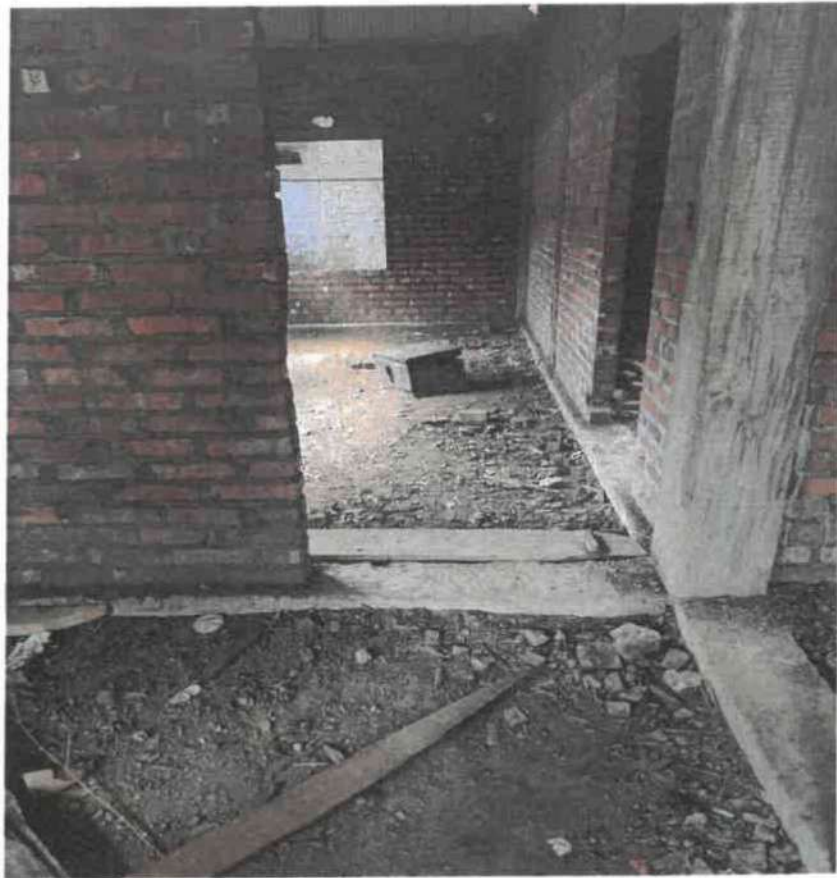

Inside view of "Construction of Teacher's Quarter at Sajik Tampak High School, Manipur"

gka
Liza R. Hell
Committee (NE)
NEC, Sect
