

**GOVERNMENT OF INDIA
NORTH EASTERN COUNCIL SECRETARIAT
NONGRIM HILLS SHILLONG-793003**

Subject: Forwarding of Inspection Report

In inviting a reference to the above subject, as requested by the concerned sector, the physical inspection of the project **“Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Manipur”** was carried out on 22/03/2021. The inspection report duly signed by Consultant (CE) and Consultant (ME), NEC is enclosed herewith. The project was sanctioned on 22-07-2016 at a total cost of Rs. 193.00 lakhs. **2(two)** instalments totalling Rs. 112.25 /- lakh was released by NEC under **MH-3601**.

The inspection, inter alia mentioned that:

- **The Project is for construction of (a) Ahalrup Panasang (266.00 Sqm), (b) Naharup Panasang (250.00 Sqm), (c) Koso Building (130.00 Sqm), (d) Toilet Block (77.00 Sqm), Entry Gate and Boundary Wall(256 m)**
- **(a) Ahalrup Panasang**
 - The works for the Ahalrup Panasang has been **completed** and till date the progress of works at site is **100%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the building constructed is more or less the **same** as that of the approved drawings in the DPR, **Ahalrup Panasang** (i.e ~**266.00 Sqm**).
 - The size of the **columns** i.e (**400 Ø**) and number of columns (**16 nos**) used at site were found to be **as per specification** mentioned in the approved DPR.
 - The consultants could not give any comments regarding the interior works including the flooring works, ceiling works etc, as it **could not be checked** because due to some religious commitment the consultants were **not allow** to enter inside the **Ahalrup Panasang**.
- **(b) Nharup Panasang**
 - The works for the Nharup Panasang has been **completed** and till date the progress of works at site is **100%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the building constructed is more or less the **same** as that of the approved drawings in the DPR, **Nharup Panasang** (i.e ~**250.00 Sqm**).
 - The size of the **columns** i.e (**400 Ø**) and number of columns (**16 nos**) used at site were found to be **as per specification** mentioned in the approved DPR.
 - The consultants could not give any comments regarding the interior works including the flooring works, ceiling works etc, as it **could not be checked** because due to some religious commitment the consultants were **not allow** to enter inside the **Nharup Panasang**.
- **(c) Koso Building**
 - The works for the **Koso Building** is in progress and till date the progress of works at site is **20-25%**. Concrete work, RCC work, Brick works, form work has been done only **upto the plinth**.
 - The plinth area of the **Koso Building** is more or less the **same** as that of the approved drawings in the DPR, (i.e ~**130.00 Sqm**),
 - Remaining works like RCC works, roofing and ceiling works, finishing works and other Miscellaneous and electrification works etc the implementing agency verbally informed that the remaining works will start simultaneously.
- **(d) Toilet Block (77.00 Sqm)**
 - The works for the **Toilet Block** is in progress till date the progress of works at site is **70%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the **Toilet Block** is more or less the **same** as that of the approved drawings in the DPR, (i.e ~**77.00 Sqm**)
 - The size of the **columns** i.e (**300x300**)sqm and number of columns (**9 nos**) used at site were found to be **as per specification** mentioned in the approved DPR.

O/C

[Handwritten Signature]
30/14

- Remaining works like flooring works, roofing and ceiling works, finishing works and other sanitary, water supply, etc the implementing agency verbally informed that the remaining works will start simultaneously.
- (e) **Entry gate**
 - The **works for the Entry gate** is almost completed and till date the progress of works at site is **95%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - Remaining finishing works like application of **plaster of paris putty and painting works** is **left to be done**.
- (f) **Boundary wall**
 - Boundary wall was found at site, till date the progress of works at site is **95%**.
 - The **length** and specification of the Boundary wall constructed is more or less the **same** as that of the approved drawing in the DPR(i.e **256 m**)
 - Remaining finishing wall with weather shield **paint** on the boundary wall is **left to be done**.
- A signboard acknowledging NEC funding was **not found** at site.
- **Remarks**
 - On scrutiny the file, there is 2 page concept note indicating the name, area, a scanty information that the entire population will be benefited and that the project will serve purely as a Human Resource Centre, that it will attract tourist which will generate income in the future.
 - The DPR starts with the site plan and has no introduction of the proposal-why the proposal is made, how are the 3 buildings to be used, how will it attract tourist and help generate income, how it will act as a Human Resource Centre, why that particular site etc. In short, it is not clear as to how the buildings are to be utilized.
 - In absence of the above information, NEC will not be able to gauge the outcome of the project and whether the project is used for the purpose for which fund was released from the consolidated fund of India.
- Sector may like to get the deviation and misrepresentations of the 3rd building clarified from the Implementing Agency and clarify as how the projects are to be utilized.

This is for information and necessary action by the concerned Sector.

Enclosure: As above

Atanu Saha
30.07.2021
(Atanu Saha)
I/o Director, (E&M)

U.O.No. NEC/EM/INSPECTION/IPR/2013/01

Dated: ...*30.07*.../2021

To,
Director (IPR), NEC

Copy to:

3. P.S to Planning Adviser, NEC for kind information of Planning Adviser - *2-3014*
4. T.D, NIC-NEC (Shri M. Nongkhlaw) for uploading the report in the NEC website

**GOVERNMENT OF INDIA
NORTH EASTERN COUNCIL SECRETARIAT
NONGRIM HILLS SHILLONG-793003**

Subject: Submission of Inspection Report of NEC funded project titled "Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg" under MH-3601.

We, Aarti Khyriemujat, Consultant (CE) and Liza R Hek, Consultant (ME) have carried out the physical inspection of the project "**Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg**" under **MH-3601** on 22/03/2021. The project was sanctioned on 22/07/2017 at a total cost of Rs.193.00 lakhs. **2 (two)** instalments totalling Rs. 112.25 /- lakh was released by NEC under **MH-3601**.

Objective of the Project:-

- Preservation of cultural heritage.
- Promotion of culture.
- Development of tourist attraction centre.
- To establish human to human relation

Indication of Works as per DPR:-

- Ahalrup Pnasang- 1 no.
- Nharup Pnasang- 1 no.
- Koso Building- 1 no.
- Toilet Block- 1 no.
- Entry Gate – 2 nos.
- Boundary Wall – 256 mts.

Proposed Beneficiaries & Outcome of the Project:-

Beneficiaries:

- The project essentially will benefit the entire population in the state and neighbouring states especially the community residing in Andro region.

Outcomes:

- The project will serve purely as Human Resource Centre. However, once the project is completed, it will attract tourist which can naturally generate income in future.

Observation mentioned in the inspection report:-

During inspection it could be seen that:

- **The Project is for construction of (a) Ahalrup Panasang (266.00 Sqm), (b) Naharup Panasang (250.00 Sqm), (c) Koso Building (130.00 Sqm), (d) Toilet Block (77.00 Sqm), Entry Gate and Boundary Wall(256 m)**
- **(a) Ahalrup Panasang**
 - The works for the **Ahalrup Panasang** has been **completed** and till date the progress of works at site is **100%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the building constructed is more or less the **same** as that of the approved drawings in the DPR, **Ahalrup Panasang** (i.e ~266.00 Sqm).
 - The size of the **columns** i.e (400 Ø) and number of columns (**16 nos**) used at site were found to be **as per specification** mentioned in the approved DPR.
 - The consultants could not give any comments regarding the interior works including the flooring works, ceiling works etc, as it **could not be checked** because due to some religious commitment the consultants were **not allow** to enter inside the **Ahalrup Panasang**.

A. Khyriemujat
19/4/21
Aarti Khyriemujat
Consultant CCE
NEC, Secretariat

Liza R. Hek
19/4/21
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

- **(b) Naharup Panasang**
 - The **works for the Naharup Panasang** has been **completed** and till date the progress of works at site is **100%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The **plinth area of the building constructed is more or less the same** as that of the approved drawings in the DPR, **Naharup Panasang (i.e ~250.00 Sqm)**.
 - The size of the **columns i.e (400 Ø)** and number of columns (**16 nos**) used at site were found to be **as per specification** mentioned in the approved DPR.
 - The consultants could not give any comments regarding the interior works including the flooring works, ceiling works etc, as it **could not be checked** because due to some religious commitment the consultants were **not allow** to enter inside the **Naharup Panasang**.
- **(c) Koso Building**
 - The **works for the Koso Building** is in progress and till date the progress of works at site is **20-25%**. Concrete work, RCC work, Brick works, form work has been done only **upto the plinth**.
 - The plinth area of the **Koso Building** is more or less the **same** as that of the approved drawings in the DPR, (i.e ~**130.00 Sqm**),
 - Remaining works like RCC works, roofing and ceiling works, finishing works and other Miscellaneous and electrification works etc the implementing agency verbally informed that the remaining works will start simultaneously .
- **(d) Toilet Block (77.00 Sqm)**
 - The **works for the Toilet Block** is in progress till date the progress of works at site is **70%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the **Toilet Block** is more or less the **same** as that of the approved drawings in the DPR, (i.e ~**77.00 Sqm**)
 - The size of the **columns i.e (300x300)sqm** and number of columns (**9 nos**) used at site were found to be **as per specification** mentioned in the approved DPR.
 - Remaining works like flooring works, roofing and ceiling works, finishing works and other sanitary, water supply, etc the implementing agency verbally informed that the remaining works will start simultaneously.
- **(e) Entry gate**
 - The **works for the Entry gate** is almost completed and till date the progress of works at site is **95%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - Remaining finishing works like application of **plaster of paris putty and painting works** is **left to be done**.
- **(f) Boundary wall**
 - Boundary wall was found at site, till date the progress of works at site is **95%**.
 - The **length** and specification of the Boundary wall constructed is more or less the **same** as that of the approved drawing in the DPR(**i.e 256 m**)
 - Remaining finishing wall with weather shield **paint** on the boundary wall is **left to be done**.
- A signboard acknowledging NEC funding was **not found** at site.

A. Mujat
19/4/21
Aarti Khymemujat
Consultant (CE)
NEC, Secretariat.


19/4/2021
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

Report of the inspection carried on 22/03/2021 for the NEC funded project “Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg”

A joint inspection of the above project was carried out by the official of NEC Secretariat, Shillong and officials of the Manipur Tribal Development Corporation Ltd., on 22/03/2021 at Imphal East, Manipur. The list of the officials present during the inspection is enclosed as Annexure-I

(I) BACKGROUND:

Name of the project:	“Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg”
Location:	Andro, Imphal East ,Manipur
Implementing Agency:	Manipur Tribal Development Corporation Ltd.
Date of Sanction:	22-07-2016
Cost of Project:	Rs. 193.00 lakh under MH-3601
NEC Share (90%):	Rs. 173.70 lakh
State Share (10%):	Rs. 19.30 lakh
NEC Share released & Dates:	1 st installment of Rs.62.25 lakh on 22/07/2016 2 nd installment of Rs.50.00 lakh on 28/02/2018
Total Amount Released by NEC :	Rs.112.25 lakh
Balance amount to be released by NEC:	Rs.61.45 lakh
State Share released :	Rs.19.30 lakh
Balance amount to be released by State:	Rs. 0.00 lakh
Status of UC for NEC share :	UC for Rs. 62.25 lakh for 1 st installment submitted on 29/09/2017 UC for Rs. 50.00 lakh for 2 nd installment submitted on 21/10/2020
Status of UC for State share :	-
Target Date of Completion:	31-03-2021

(II) Aims/Objectives of the Project:-

- Preservation of cultural heritage.
- Promotion of culture.
- Development of tourist attraction centre.
- To establish human to human relation

A. Rijat
19/4/21
Aarti Khysiemujat
Consultant (CEB)
NEC, Secretariat

[Signature]
19/4/2021
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

(III) Observations/ Status of works (Physical Achievements):-

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
(A) AHALRUP PANASANG					
1	Earthworks	42094.5	<ul style="list-style-type: none">• During inspection it could be seen that the structure of the building is completed, thus it can be assume that works related to earthwork excavation and filling has been done.	•NIL	<ul style="list-style-type: none">• As the earthwork excavation and filling have been completed the consultant could not give any comments.
2	Concrete works	175175.67	<ul style="list-style-type: none">• Concrete works in foundation and plinth etc, has been done at site.	•NIL	<ul style="list-style-type: none">• As the concrete works has been completed the consultant could not give any comments regarding the design mix.
3	Reinforced Cement Concrete Works.	1453166.88	<ul style="list-style-type: none">• Works related to RCC has been completed	•NIL	<ul style="list-style-type: none">• As the RCC work is completed the consultant could not give any comments regarding the design mix.
4	Form work	185693.78	<ul style="list-style-type: none">• Form work on foundations, footings, bases of columns, pile caps, rafts, beams, etc has been completed.	• NIL	<ul style="list-style-type: none">• As the form work was completed the consultant could not give any comments.
5	Brick work in Cement Mortar with fine sand	310583.6	<ul style="list-style-type: none">• Brickwork has been done at site.	• NIL.	<ul style="list-style-type: none">• The consultant could not give any comments regarding the type of brick work and the design mix as the brick work was completed.
6	Wood work	88896.08	<ul style="list-style-type: none">• Woodwork has been done at site.	• NIL	<ul style="list-style-type: none">• NIL
7	Steel Work	305214.26	<ul style="list-style-type: none">• Steel works including application of priming coat and painting works of the steel and steel surfaces has been done at site.	• NIL	<ul style="list-style-type: none">• As Steel works including application of priming coat and painting works of the steel and steel surfaces has been done at site the consultant could not give any comments.
8	Flooring	477607.8	<ul style="list-style-type: none">• Through verbal discussions the beneficiaries informed that flooring works has been done as specified in the approved	• NIL	<ul style="list-style-type: none">• The consultants could not give any comments regarding the interior works including the flooring works as due to some religious commitment

Aarti Khysimujat
19/11/21
Aarti Khysimujat
Consultant CCE
NEC, Secretariat

Liza R. Hek
19/11/2021
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
			DPR.		the consultants were not allow to enter inside the Panasang.
9	Roofing & Ceiling	533158.81	• Roofing & ceiling works has been completed.	• NIL	• The consultants could not give any comments regarding the interior ceiling works as due to some religious commitment the consultants were not allow to enter inside the Panasang.
10	Finishing	235065.04	• Finishing works including painting on walls and wood surfaces has been done at site.	• NIL	• NIL
11	Miscellaneous	52239.50	• Plinth protection works has been completed at site.	• NIL	• The plinth area of the Ahalrup Panasang is more or less the same as that of the approved drawing in the DPR(i.e ~266.00 Sqm)
	Total For Civil Works(1 to 11)	3852924.00			
	Internal Electrical Work's -10%	385292.40			
	Total (X)	4238216.4			
(B) NAHARUP PANASANG					
1	Earthworks	40055.16	• During inspection it could be seen that the structure of the building is completed, it can be assume that works related to earthwork excavation and filling has been done.	• NIL	• As the earthwork excavation and filling have been completed the consultant could not give any comments.
2	Concrete works	167143.42	• Concrete works in foundation and plinth etc, has been done at site.	• NIL	• As the concrete works has been completed the consultant could not give any comments regarding the design mix.

A. Mijat
19/4/21
Aarti Khysimmijat
Consultant CCE
NEC, Secretariat

[Signature]
19/4/2021
 Liza R. Hek
 Consultant (ME)
 North Eastern Council Secretariat

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
3	Reinforced Cement Concrete Works.	1419498.32	• Works related to RCC has been completed	• NIL	• As the RCC work is completed the consultant could not give any comments regarding the design mix.
4	Form work	180134.65	• Form work on foundations, footings, bases of columns, pile caps, rafts, beams, etc has been completed.	• NIL	• As the form work was completed the consultant could not give any comments .
5	Brick work in Cement Mortar with fine sand	283241.900	• Brickwork has been done at site.	• NIL.	• As the brick work was completed the consultant could not give any comments regarding the type of brick work and the design mix.
6	Wood work	82299.280	• Woodwork has been done at site.	• NIL	• NIL
7	Steel Work	282019.120	• Steel works including application of priming coat and painting works of the steel and steel surfaces has been done at site.	• NIL	• As Steel works including application of priming coat and painting works of the steel and steel surfaces has been done at site the consultant could not give any comments.
8	Flooring	450312.090	• Flooring works has been completed as informed by the beneficiaries.	• NIL	• The consultants could not give any comments regarding the interior works including the flooring works as due to some religious commitment the consultants were not allow to enter inside the Panasang.
9	Roofing & Ceiling	474316.160	• Roofing & ceiling works has been completed.	• NIL	• The consultants could not give any comments regarding the interior ceiling works as due to some religious commitment the consultants were not allow to enter inside the Panasang.
10	Finishing	211683.410	• Finishing works including painting on walls and wood surfaces has been done at site.	• NIL	• NIL

A. Mujat
19/4/21
Aarti Khyrimujat
Consultant (CE)
NEC, Secretariat

Liza R. Hek
19/4/2021
 Liza R. Hek
 Consultant (ME)
 North Eastern Council Secretariat

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
11	Miscellaneous	44163.630	<ul style="list-style-type: none"> Plinth protection works has been completed at site. 	<ul style="list-style-type: none"> NIL 	<ul style="list-style-type: none"> The plinth area of the Naharup Panasang is more or less the same as that of the approved drawing in the DPR((i.e ~250.00 Sqm)
	Total For Civil Works(1 to 11)	3634868.00			
	Internal Electrical Work's -10%	363487.00			
	Total (X)	3998355.00			
(C) KOSO BUILDING					
1	Earthworks	23416.78	<ul style="list-style-type: none"> During inspection it could be seen that the construction of the building is in progress, it can be assume that works related to earthwork excavation and filling has been done. 	<ul style="list-style-type: none"> NIL 	<ul style="list-style-type: none"> As the earthwork excavation and filling have been completed the consultant could not give any comments.
2	Concrete works	93874.16	<ul style="list-style-type: none"> Concrete works in foundation and plinth etc, has been done at site. 	<ul style="list-style-type: none"> NIL 	<ul style="list-style-type: none"> As the concrete works has been completed the consultant could not give any comments regarding the design mix.
3	Reinforced Cement Concrete Works.	537999.0	<ul style="list-style-type: none"> Works related to RCC in the foundation, footings has been done at site. 	<ul style="list-style-type: none"> RCC works in columns, pillars, piers, abutments, post, struts etc. 	<ul style="list-style-type: none"> As the RCC work upto the plinth level has been completed the consultant could not give any comments regarding the design mix.
4	Form work	50811.92	<ul style="list-style-type: none"> Form work on foundations, footings, bases of columns, has been completed. 	<ul style="list-style-type: none"> Form work for columns, pillars posts and struts. 	<ul style="list-style-type: none"> NA
5	Brick work in Cement Mortar with fine sand	102360.5	<ul style="list-style-type: none"> Brickwork has been done at site. 	<ul style="list-style-type: none"> NIL. 	<ul style="list-style-type: none"> As the brick work was completed the consultant could not give any comments regarding the type of brick work and the design mix.

A. Mujat
19/4/21
Aarti Khyrie Mujat
Consultant CCE
NEC, Secretariat

Liza R. Hek
19/4/2021
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
6	Steel Work	206027.42	• Not yet started.	• Steel works.	• NA
7	Flooring	225322.6	• Not yet started.	• Flooring works.	• NA
8	Roofing & Ceiling	168487.6	• Not yet started.	• Roofing & ceiling works.	• NA
9	Finishing	7280.2	• Not yet started.	• Finishing works including weather shield painting on new work (three or more coats).	• NA
10	Miscellaneous	232497.00	• Not yet started.	• Providing and fixing stainless steel railing with SS 304 grade tubular section thick hollow pipes.	• The plinth area of the Koso Building is more or less the same as that of the approved drawing in the DPR(i.e ~130.00 Sqm)
	Total For Civil Works(1 to 10)	1648077.00	• Not yet started	• Providing, fitting and fixing anodized aluminum windows, doors, ventilators etc.	• NA
	Internal Electrical Work's -10%	164807.70			
	Total (X)	1812885.00			
(D) PUBLIC TOILET BLOCK					
1	Earthworks	19667.02	• During inspection it could be seen that the construction of the toilet block is in progress, it can be assume that works related to earthwork excavation and filling has been done.	• NIL	• As the earthwork excavation and filling have been completed the consultant could not give any comments.
2	Concrete works	67244.36	• Concrete works in foundation and plinth etc, has been done at site.	• NIL	• As the concrete works has been completed the consultant could not give any comments regarding the design mix.

A. Mijat
19/4/21
Aarti Khyrie Mijat
Consultant CCE
NEC, Secretariat

[Signature]
19/4/2021
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
3	Reinforced Cement Concrete Works.	826217.1	• Works related to RCC has been completed	• NIL	• As the RCC work is completed the consultant could not give any comments regarding the design mix.
4	Form work	120954.00	• As the frame of the structure is completed it can be said that Form work has been done at site.	• NIL	• As the form work was completed the consultant could not give any comments .
5	Brick work in Cement Mortar with fine sand	295988.7	• Brickwork for the foundation and superstructure has been done at site.	• NIL.	• As the brick work was completed the consultant could not give any comments regarding the type of brick work and the design mix.
6	Wood work	166600.1	• Woodwork has been done at site.	• NIL	• NIL
7	Flooring	253983.6	• Flooring works has not yet started.	• Flooring works	• NA
8	Roofing & Ceiling	75046.84	• Roofing & Ceiling works is in progress.	• Roofing & Ceiling works	• NA
9	Finishing	215628.4	• Not yet started	• Finishing works	• NIL
10	Miscellaneous	14955	• Plinth protection works has been done at site.	• NIL	• The plinth area of the Toilet Block is more or less the same as that of the approved drawing in the DPR(i.e ~77.00 Sqm)
	Total For Civil Works(1 to 11)	2056285.00			
	Internal Electrical Work's -12.5%	257035.60			
	Water Supply, Sanitary and Drainage Work's - 10%	205628.50			

A. Mujat
19/11/21
Aarti Khejri Moriyat
Consultant CCEB
NEC, Secretariat

Liza R. Hek
19/11/21
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
	Total (X)	2518950.00			
(E) ENTRY GATE					
1	Earthworks	5932.62	<ul style="list-style-type: none"> • During inspection, it was could be seen that the entry gate was constructed ,thus it can be assume that works related to earthwork excavation and filling has been done. 	• NIL	<ul style="list-style-type: none"> • As the earthwork excavation and filling have been completed the consultant could not give any comments.
2	Concrete works	24481.36	<ul style="list-style-type: none"> • Concrete works in foundation and plinth etc, has been done at site. 	• NIL	<ul style="list-style-type: none"> • As the concrete works has been completed the consultant could not give any comments regarding the design mix.
3	Reinforced Cement Concrete Works.	584632.60	<ul style="list-style-type: none"> • Works related to RCC has been completed 	• NIL	<ul style="list-style-type: none"> • As the RCC work is completed the consultant could not give any comments regarding the design mix.
4	Form work	97767.02	<ul style="list-style-type: none"> • As the construction of the entry gate was fully completed it could be said that form work has been done. 	• NIL	<ul style="list-style-type: none"> • As the form work was completed the consultant could not give any comments
5	Brick work in Cement Mortar with fine sand	78546.74	<ul style="list-style-type: none"> • Brickwork has been done at site. 	• NIL.	• NIL
6	Wood work	19637.39	<ul style="list-style-type: none"> • Woodwork has been done at site. 	• NIL	<ul style="list-style-type: none"> • The consultant could not give any comments regarding the quality of wood used as the wood work has already been done at site.
7	Flooring	6539.28	<ul style="list-style-type: none"> • Flooring works has been completed. 	• NIL	<ul style="list-style-type: none"> • The consultant could not give any comments as the flooring work has already been done.
8	Roofing & Ceiling	6584.85	<ul style="list-style-type: none"> • Roofing & ceiling works has been completed. 	• NIL	• NIL
9	Finishing	73547.62	<ul style="list-style-type: none"> • Plastering works has been done at site . 	<ul style="list-style-type: none"> • Application of plaster of paris putty and painting works is left 	• NIL

A. Mujat
19/4/21
Aarti Khysimmujat
Consultant (CE)
NEC, Secretariat

[Signature]
19/4/2021
 Liza R. Hek
 Consultant (ME)
 North Eastern Council Secretariat

Sl. No	Approved items of Works	Approved Cost	Achievement found as on date of inspection	Item of work left for completion	Any Deviation with reason
				to be done.	
10	Miscellaneous	15516.00	<ul style="list-style-type: none"> Plinth protection works has been completed at site. 	<ul style="list-style-type: none"> NIL 	<ul style="list-style-type: none"> As the Plinth protection works has been completed the consultant could not give any comments regarding the brick class and the design mix.
	Total For Civil Works(1 to 10)	893753.70	<ul style="list-style-type: none"> Not yet started 	<ul style="list-style-type: none"> Providing, fitting and fixing anodized aluminum windows, doors, ventilators etc. 	<ul style="list-style-type: none"> NA
	Internal Electrical Work's -10%	111719.00			
	Total (X)= Cost of 1 No Entry Gate	1005474			
	Cost of 2 No Entry Gate	2010946.00			
	(F) BOUNDARY WALL	3061248.00	<ul style="list-style-type: none"> Boundary wall was found at site 	<ul style="list-style-type: none"> Finishing wall with weather shield paint on the boundary wall is left to be done. 	<ul style="list-style-type: none"> The length and specification of the Boundary wall constructed is more or less the same as that of the approved drawing in the DPR(i.e 256 m)
	Labour cess, agency charge, contingency etc.	1675857.00			
	GRAND TOTAL	19316457.00			

(IV) Location Of The Project:

Latitude: 24°45.046' N

Longitude: 94°2.733'E

A. Mujat
19/4/21
Aarti Khyrie Mujat
Consultant (CE)
NEC, Secretariat.

[Signature]
19/4/2021
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

(V) Overall Remarks and Suggestions:-

During inspection the following observations were made:

- **The Project is for construction of (a) Ahalrup Panasang (266.00 Sqm), (b) Naharup Panasang (250.00 Sqm), (c) Koso Building (130.00 Sqm), (d) Toilet Block (77.00 Sqm), Entry Gate and Boundary Wall(256 m)**
- **(a) Ahalrup Panasang**
 - The **works for the Ahalrup Panasang** has been **completed** and till date the progress of works at site is **100%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the building constructed is more or less the **same** as that of the approved drawings in the DPR, **Ahalrup Panasang** (i.e ~266.00 Sqm).
 - The size of the **columns** i.e (400 Ø) and number of columns (16 nos) used at site were found to be **as per specification** mentioned in the approved DPR.
 - The consultants could not give any comments regarding the interior works including the flooring works, ceiling works etc, as it **could not be checked** because due to some religious commitment the consultants were **not allow** to enter inside the **Ahalrup Panasang**.
- **(b) Naharup Panasang**
 - The **works for the Naharup Panasang** has been **completed** and till date the progress of works at site is **100%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the building constructed is more or less the **same** as that of the approved drawings in the DPR, **Naharup Panasang** (i.e ~250.00 Sqm).
 - The size of the **columns** i.e (400 Ø) and number of columns (16 nos) used at site were found to be **as per specification** mentioned in the approved DPR.
 - The consultants could not give any comments regarding the interior works including the flooring works, ceiling works etc, as it **could not be checked** because due to some religious commitment the consultants were **not allow** to enter inside the **Naharup Panasang**.
- **(c) Koso Building**
 - The **works for the Koso Building** is in progress and till date the progress of works at site is **20-25%**. Concrete work, RCC work, Brick works, form work has been done only **upto the plinth**.
 - The plinth area of the **Koso Building** is more or less the **same** as that of the approved drawings in the DPR, (i.e ~130.00 Sqm),
 - Remaining works like RCC works, roofing and ceiling works, finishing works and other Miscellaneous and electrification works etc the implementing agency verbally informed that the remaining works will start simultaneously .
- **(d) Toilet Block (77.00 Sqm)**
 - The **works for the Toilet Block** is in progress till date the progress of works at site is **70%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - The plinth area of the **Toilet Block** is more or less the **same** as that of the approved drawings in the DPR, (i.e ~77.00 Sqm)

A. Mijat
19/4/21
Aarti Khysimmijat
Consultant C.E.E
NEC, Secretariat

Liza R. Hek
19/4/2021
Liza R. Hek
Consultant (MC)
North Eastern Council Secretariat

- The size of the **columns** i.e (300x300)sqm and number of columns (**9 nos**) used at site were found to be **as per specification** mentioned in the approved DPR.
- Remaining works like flooring works, roofing and ceiling works, finishing works and other sanitary, water supply, etc the implementing agency verbally informed that the remaining works will start simultaneously.
- **(e) Entry gate**
 - The **works for the Entry gate** is almost completed and till date the progress of works at site is **95%**, thus structural details such as Reinforcement details, and concrete mix design etc **could not be checked**.
 - Remaining finishing works like application of **plaster of paris putty** and **painting works** is **left to be done**.
- **(f) Boundary wall**
 - Boundary wall was found at site, till date the progress of works at site is **95%**.
 - The **length** and specification of the Boundary wall constructed is more or less the **same** as that of the approved drawing in the DPR(**i.e 256 m**)
 - Remaining finishing wall with weather shield **paint** on the boundary wall is **left to be done**.
- A signboard acknowledging NEC funding was **not found** at site.

The outcomes and beneficiaries of the project can be briefly listed as below:

○ **Beneficiaries:**

- The project essentially will benefit the entire population in the state and neighbouring states especially the community residing in Andro region.







Outcomes:

- The project will serve purely as Human Resource Centre. However, once the project is completed, it will attract tourist which can naturally generate income in future.

A. Khyat
19/4/21
Aarti Khyat
Consultant (CE)
NEC, Secretariat.


Calicut
 Liza R. Hek
 Consultant (ME)
 North Eastern Council Sec


List of officials who were present during the inspection of NEC funded project
 "Infrastructure Development for Preservation of Panam Ninghou Immortal for and different
 Historical Monuments in and around, Imphal East Manipur" on 22/03/2021

Sl. No.	Name	Contact No. & Email id	Designation & Organisation/Department	Signature
1.	Romesh Tomagbam	9612391613	JE/MTDC	 22/03/2021
2.	Th. Ruben	8119800669 RubenFamoe@gmail.com	JE/MTDC	 22/03/2021
3.	M. Anujadon	9366761271	contractor	 22/03/21
4.	N. Naba		Temple board	 N. Naba
5.	Aarti Khynemmyat	8974593379	Consultant (CE)/NEC	 Aarti
6.	Liza R. Heh	993616775	Consultant (ME) NEC	 Liza
7.				
8.				
9.				
10.				



Latitude: 24 45.046'N
Longitude: 94 2.733'E

Overall view of the Ahalrup Panasang and Naharup Panasang Building for the project “ Infrastrusture development for preservation of Panam Ningthou Immortal fire and different historical monuments in an around Andro”.

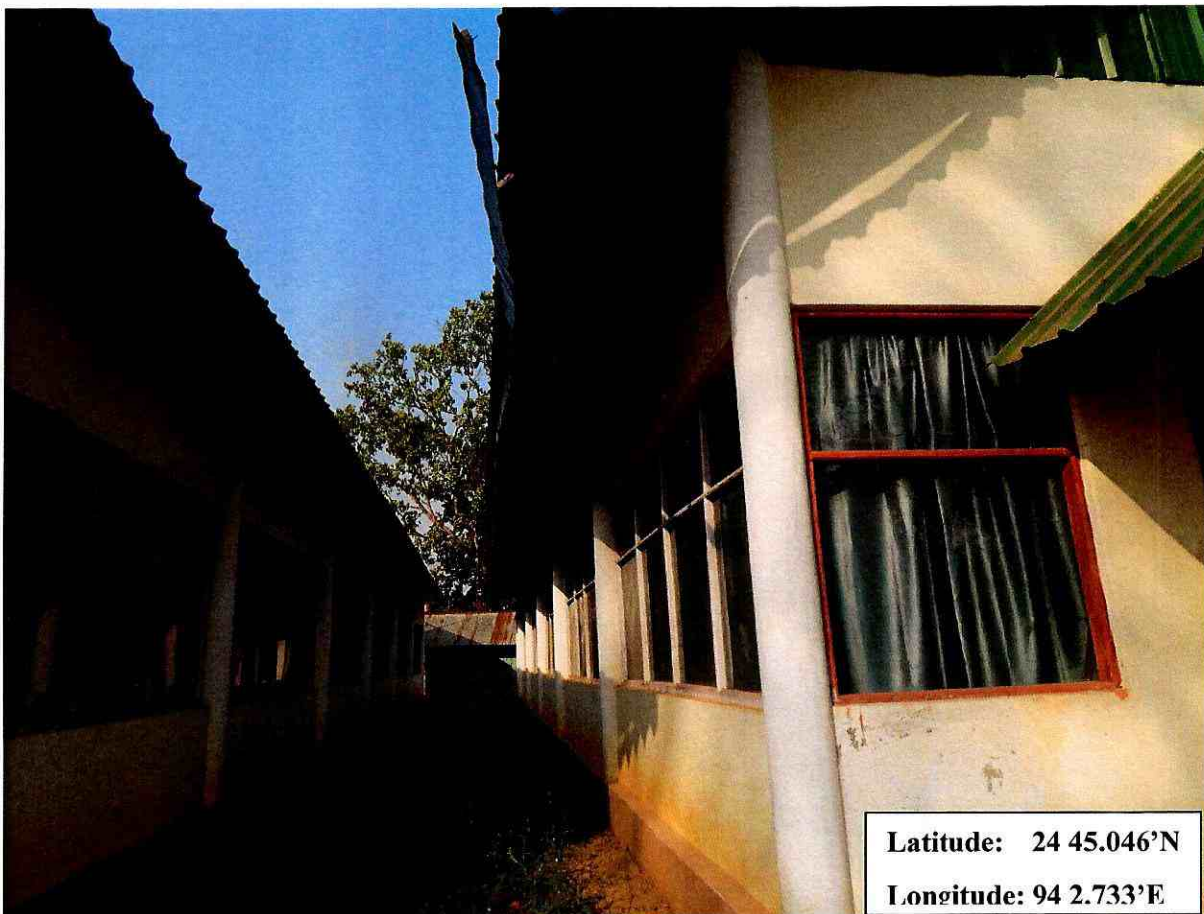

Latitude: 24 45.046'N
Longitude: 94 2.733'E

Side view of the Ahalrup Panasang and Naharup Panasang Building for the project “ Infrastrusture development for preservation of Panam Ningthou Immortal fire and different historical monuments in an around Andro”.

Ak. Myat
 19/11/21
 Aarti Khyiemmyat
 Consultant (CE),
 NEC, Secretariat

[Signature]
 19/11/21
 Liza R. Hek
 Consultant (ME)
 North Eastern Council Secretariat



Latitude: 24 45.046'N
Longitude: 94 2.733'E

Front view of the Ahalrup Panasang Building for the project “Infrastrusture development for preservation of Panam Ningthou Immortal fire and different historical monuments in an around Andro”.



Latitude: 24 45.046'N
Longitude: 94 2.733'E

Backview of the Ahalrup Panasang Building for the project “Infrastrusture development for preservation of Panam Ningthou Immortal fire and different historical monuments in an around Andro”.

Ak. mijat
19/4/21
Aarti Khyreemijat
Consultant (CE)
NEC, Secretariat

[Signature]
19/4/2021
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat



Latitude: 24 45.046'N
Longitude: 94 2.733'E

Photo of the boundary wall for the project “Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg”




Latitude: 24 45.046'N
Longitude: 94 2.733'E

Overall view of the Koso building under construction for the project “Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg”

Ak. Mijal
19/11/21
Aarti Khyrie Mijal
Consultant CCE
NEC, Secretariat.

Liza R. Hek
17/11/21
Liza R. Hek
Consultant (ME)
North Eastern Council Secretariat

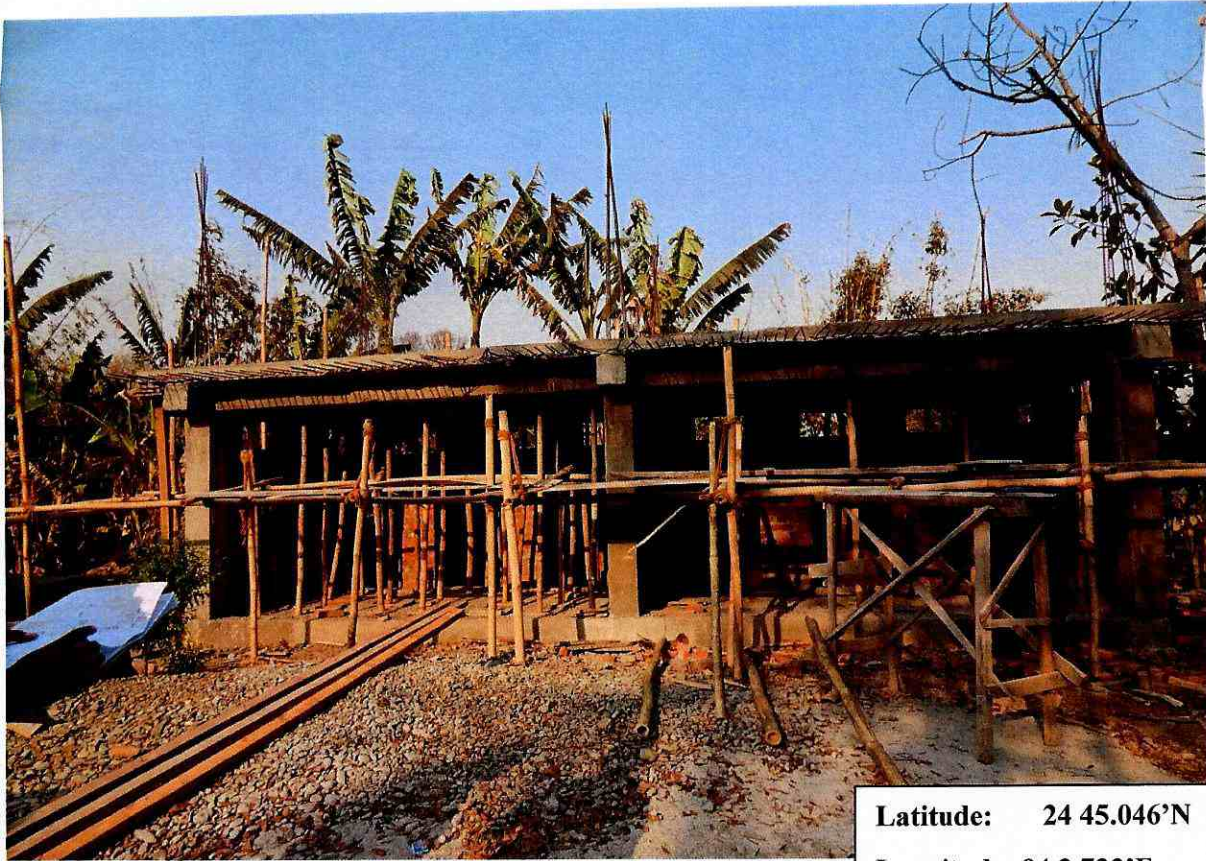

Latitude: 24 45.046'N
 Longitude: 94 2.733'E

Overall view of the toilet block under construction for the project "Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg"




Latitude: 24 45.046'N
 Longitude: 94 2.733'E

Photo showing the brickwork of the toilet block for the project "Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg"


A. Mijal
 19/4/21
 Aarti Khyiemmijal
 Consultant (CE)
 NEC Secretariat

Liza R. Hek
 19/4/2021
 Liza R. Hek
 Consultant (ME)
 North Eastern Council Secretariat

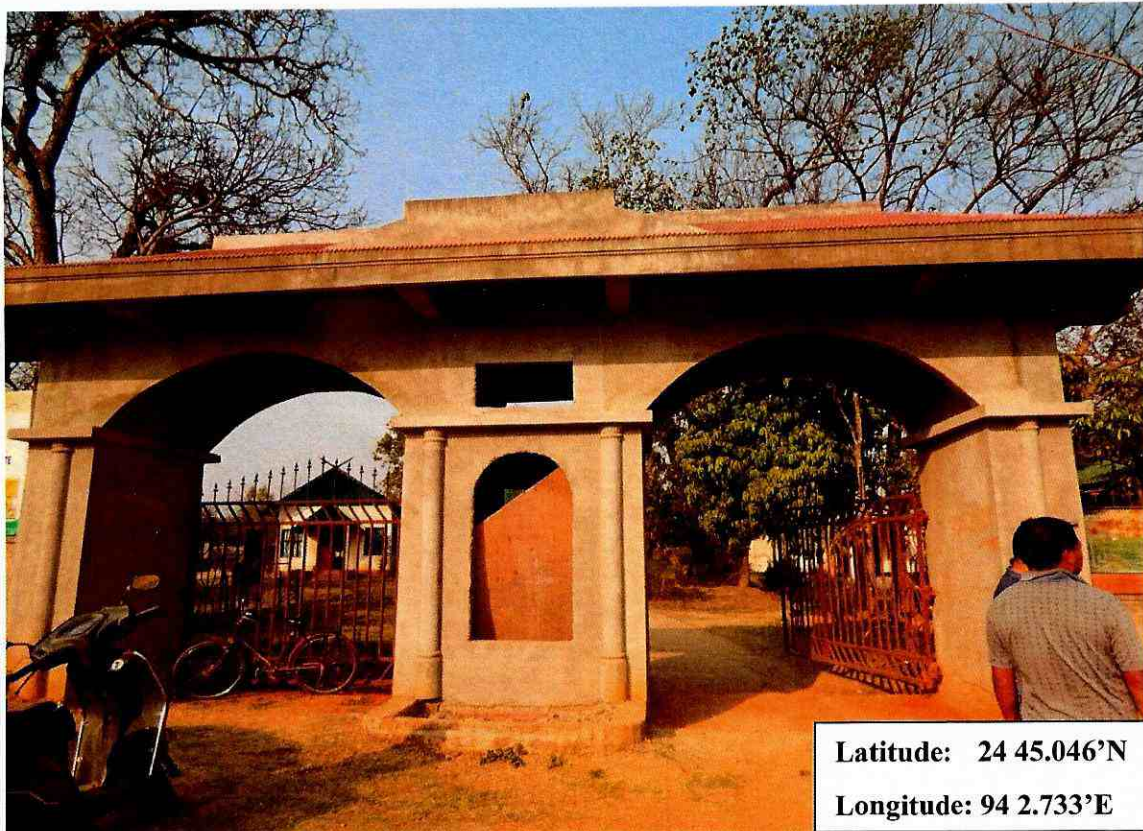

Latitude: 24 45.046'N
Longitude: 94 2.733'E

Photo showing the entry gate for the project “Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg”

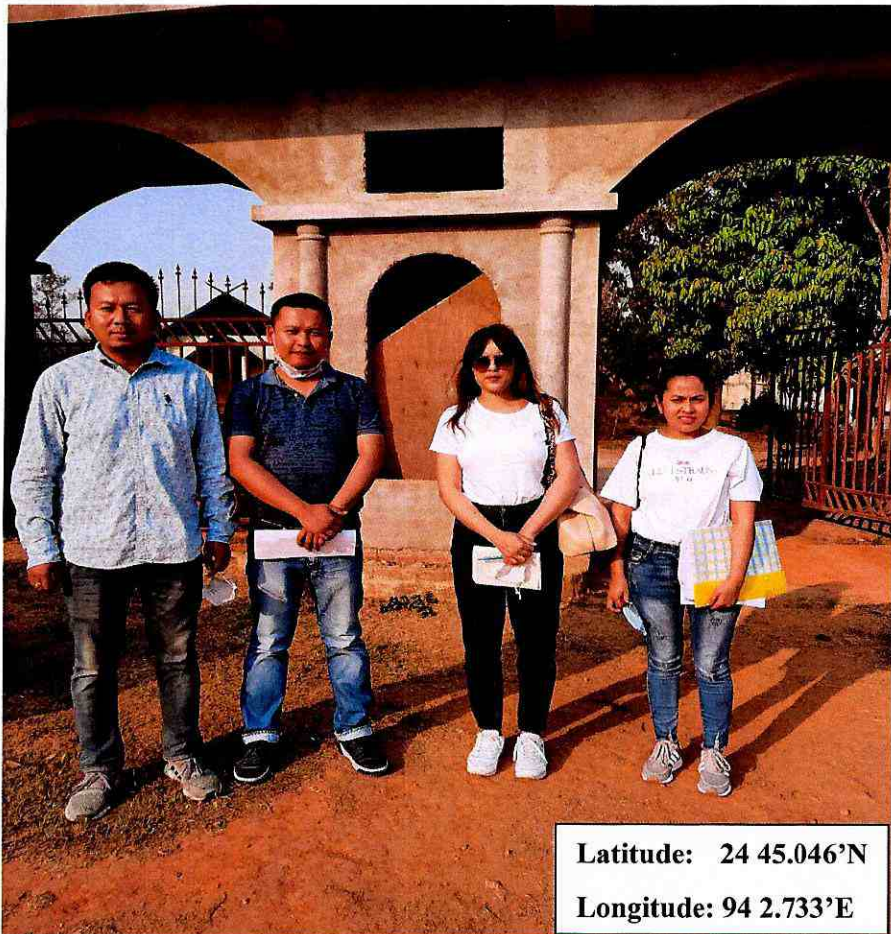

Latitude: 24 45.046'N
Longitude: 94 2.733'E

Photo of the inspection team along with the officials of the implementing department at the project site for the project “Infrastructure Development for Preservation of the Panam Ningthou immortal fire and different historical monuments in and around Andro-Reg”

A. Mijal
19/12/21
Asst. Xhruic mmyiat
Consultant CGEY
NEC Secretariat.

[Signature]
Liza R. Hek
 Consultant (ME)
 North Eastern Council Secretariat
