

**GOVERNMENT OF INDIA
NORTH EASTERN COUNCIL SECRETARIAT
NONGRIM HILLS: SHILLONG - 793003**

Subject: Forwarding of Inspection Report.

In inviting a reference to the above subject, as requested by the concerned Sector, the physical inspection of the project "**Establishment of Kiwi Garden at Dora Morey at HIJA Village under Lower Subansiri District, Arunachal Pradesh,**" was carried out in Ziro, Arunachal Pradesh. The inspection report duly signed by the Consultant (CE) and Consultant (EE), NEC and HDO Horticulture Department, Arunachal Pradesh is enclosed herewith. The project was sanctioned on 23/03/2012 at a total cost of Rs. 309.78 lakhs (NEC's share Rs. 278.80 lakhs and State Share Rs. 30.98 lakhs). Two installments totalling Rs. 225.00 lakhs was released by the NEC.


The inspection report, inter alia, mentions that:

- During inspection it could be seen that the progress of work was slow.
- It may be noted that the target date of completion as given in the DPR was 2(Two) years from the date of Sanction. Hence, the project has already suffered from time overrun.
- The Implementing Agency informed the Inspection team that the area covered till date (10/01/2017) for kiwi plantation was approximately 46 Hectares. The implementing agency also stated that the land development for new areas was still going on and it would cover more than 62 hectares.
- Implementing agency stated that till now 14 nos. of beneficiaries were benefitted and it was suggested to involve all listed beneficiaries as early as possible so that project would be successful and the whole community would be beneficial. 21 no's of beneficiaries yet to be benefitted.
- No State Share has been released so far.
- UC and progress report for the 2nd Installment are also pending.
- NEC funding was found to be acknowledged.

The concerned sector should write to the Implementing Agency regarding the above mentioned points and the target date of completion as given in the DPR which was 2(Two) years from the date of Sanction. Hence, the project has already suffered from time overrun.

This is for information and necessary action by the concerned sector.

Enclosure: As above.


(W. Synrem)
Economic Adviser (E&M)


U.O.No.NEC/EM/INSPECTION/Agri&Allied/2012/28/Vol. 1
Dated: the 07th/02/2017

To,

Adviser (Agri & Allied), NEC

Copy to,

1. P.S to Planning Adviser, NEC for kind information of Planning Adviser
2. PSA, NIC-NEC (Shri M. Nongkhlaw) for uploading the report with photograph on NEC website.


7/2/17 ISSUED

Report of the inspection carried on 10 / 01 /2017 for the NEC funded project "Establishment of Kiwi Garden at Dora Morey at HIJA Village under Lower Subansiri District ,Arunachal Pradesh".

A joint inspection of the above project was carried out by an officials of NEC Secretariat, Shillong and officials of Horticulture Department, Govt. of Arunachal Pradesh on 10/01/2017 at Dora Morey at HIJA Village under Lower Subansiri District . The list of the officials present during the inspection is enclosed as Annexure-I, the photographs taken during the time of inspection is enclosed as Annexure-II & statement showing the beneficiaries list till date (10/01/2017) given by the Implementing Agency is enclosed as Annexure-III

(I) BACKGROUND:

Name of the project:	Establishment of Kiwi Garden at Dora Morey at HIJA Village under Lower Subansiri District ,Arunachal Pradesh
Location:	Dora Morey at HIJA Village under Lower Subansiri District ,Arunachal Pradesh
Implementing Agency:	Department of Horticulture , Govt. of Arunachal Pradesh
Date of Sanction:	23 / 03 /2012
Cost of Project:	Rs.309.78 lakhs
NEC Share (90%):	Rs.278.80 lakhs
State Share (10%):	Rs. 30.98 lakhs
NEC Share released & Dates:	1 st installment of Rs. 155.00 lakhs on 23 / 03/2012 2 nd installment of Rs. 70.00 lakhs on 15/ 06 /2015
Total Amount Released:	Rs. 225.00 lakhs
Balance amount to be released by NEC:	Rs. 53.80 lakhs
State Share released :	Rs. 0.00 lakhs
Balance amount to be released by State:	Rs. 30.98 lakhs
Status of UC for NEC share :	UC for Rs.155.0 lakhs for 1 st installment submitted on 04 / 11 /201 3 <u>UC for Rs 70.00 lakhs for 2nd installment Pending</u>
Status of UC for State share :	State share not released.
Status of Progress Report:	Progress Report of 1 st Installment was submitted on 04/11/2013 <u>Progress Report of 2nd Installment is still Pending</u>

Target Date of Completion:	Two years from the date of sanction

(II) Aims/Objectives of the Project: To establish organic cultivation of kiwi in the hills of Arunachal Pradesh .

(III) Observations/ Status of works as on 10 / 01 /2017 (Physical Achievements):


The project is to establishment of Kiwi Garden at Dora Morey at HIJA Village under Lower Subansiri District ,Arunachal Pradesh.

SL.no.	Scope of Work	Remarks after Site Inspection
1.	Land Development including jungle clearing etc.	During inspection it could be seen that land development including jungle clearing was completed in that area where kiwi was planted which was comprising of Two no. of hillocks .Implementing agency informed the Inspection Team that the area covered till date (i.e. 10/01/2017) for kiwi plantation was approximately 46 Hectares .The implementing agency also stated that the land development for new areas was still going on and it would cover more than 62 hectares.
2.	Fencing with locally available material	During inspection it could be seen that implementing agency did the fencing with locally available material i.e with wooden pole and barbered wire where it was required.
3.	Pit Digging ,Refilling, Planting etc.	It was found that Pit digging, refilling, planting works were done properly.
4.	Improved Kiwi Fruit Cutting 10% Mortality	Implementing agency informed the inspection team that they had done this work and this work was an ongoing process and they used to collect saplings from Nursery and planted where the plant died. New planted saplings were found by the inspection team in few areas during inspection.
5.	Cost of intercultural operation, watering etc.	During inspection it could be seen that implementing agency installed G.I. watering pipe for providing irrigation purpose.


6.	Fencing Material(Barbered Wire)	During inspection it could be seen that implementing agency did the fencing with Barbered Wire in many places but it could also be seen that many areas they had not used barbered wire instead of using barbered wire they dig the soil upto 1 mtr. to protect the garden from Mithun (one local type of Bullock).
7.	Organic Plant protection Material	During inspection Implementing agency stated that the Kiwi Garden at Dora Morey at Hija Village was fully organic and they were only using organic plant protection material in that garden. They informed the visiting inspection team that they were now preparing to get organic certification for this garden.
8.	G.I. Wire for pergola making(7 Running lines.)	During inspection it could be seen that implementing agency made the pergola for kiwi trees for their growth and expansion but many pergola were tied with 6 G.I. wire lines.
9.	Iron Tangle posts to support Pergola	During inspection it could be seen that implementing agency installed iron Tangle posts to support Pergola, it was also noticed during inspection that they installed concrete T-shape posts for the better support of Pergola.
10.	Garden Tools	During inspection time, only two (2) out of 14 beneficiaries met the inspection team and they stated that they have received garden tools from Implementing department. Their names are at Sl. No – 2 and 3 of Annexure I
11.	Organic Manure/Farm Yard Manure	During inspection it could be seen that implementing agency made a special chamber for Manure/Farm Yard and it was fully covered and the beneficiaries informed that it was 3 years old.

Location:- Dora Morey at HIJA Village Latitude N 27.57971 °
Longitude E 93.79983 °


During inspection it could be seen that the progress of work was very slow. It may be noted that the target date of completion as given in the DPR was 2(Two) years from the date of Sanction .Hence, the project has already suffered from time overrun. The Implementing Agency informed the Inspection team that the area covered till date (10/01/2017) for kiwi plantation was approximately 46 Hectares .The implementing agency also stated that the land development for new areas was still going on and it would cover more than 62 hectares. Implementing agency stated that till now 14 nos. of beneficiaries were benefitted and it was suggested to involve all listed beneficiaries as early as possible so that project would be successful and the whole community would be beneficial. Sign board was there but stating all the details like name of the project, approved cost of the project, funded by ,implemented by, date of commencement of work ,date of completion etc. was required .



(PuraObing)
Horticulture Development Officer
Horticulture Department, Arunachal Pradesh
Ziro
Lower Subansiri Distt. (A.P.)







(Abhijit Sarkar)
Consultant (EE)
NEC Secretariat, Shillong



(Jereel Nicholas J. Kharbhih)
Consultant (CE)
NEC Secretariat, Shillong

List of officials who were present during the inspection of NEC funded project "Establishment of Kiwi Garden at Dora Morey at Hija Village under Lower Subansiri District, Arunachal Pradesh. on~~11/2016~~ 10/01/2017

Sl. No.	Name	Contact No. & Email id	Designation & Organisation/Department	Signature
1.	Pura Obing	PURAOBING 16 of mid. con.	Horticulture Development Officer (HDB)	 10/01/17
2.	Puna yanga		Beneficiaries	P. yanga 10/01/17
3.	Puna yassing		Beneficiaries	 10/01/17
4.	ABHJIT SARKAR	8132853127	Consultant (EE) NEC	 10/01/17
5.	Seriel Khorblit	9136535665	Consultant (CE) NEC	
6.				
7.				
8.				
9.				
10.				



View of Organic Manuare/Farm Yard



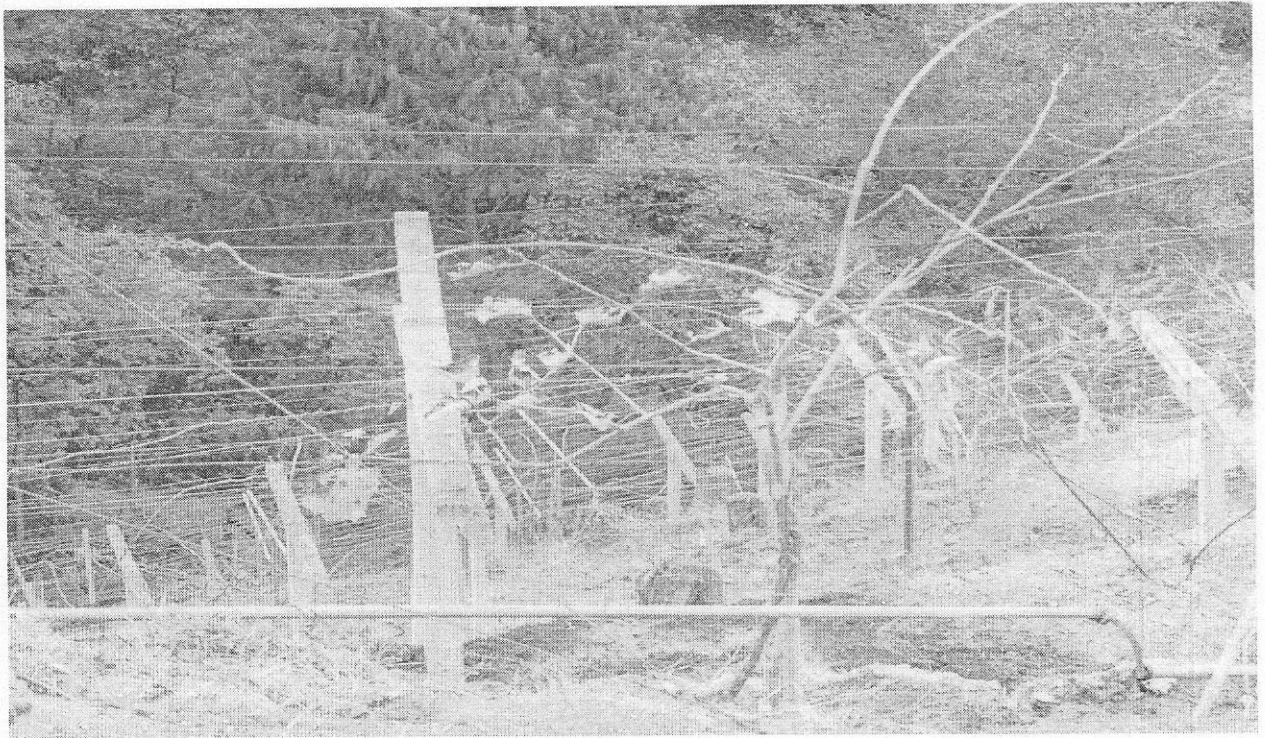
View of Inspection team infront of the entrance gate of Kiwi garden



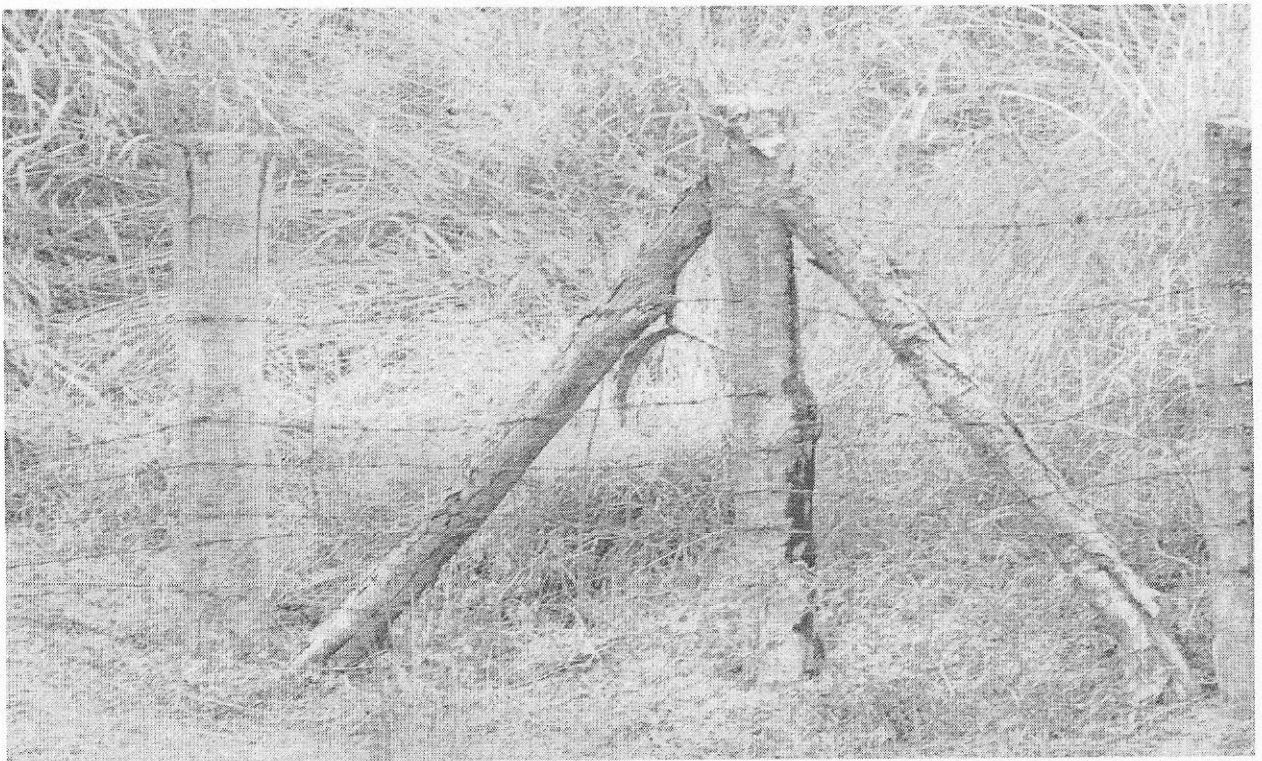
View of Kiwi plantation at Dora Morey at Hija village



View of Iron Tangle post and C.C. Tee post inside the Kiwi Garden



View of G.I. Wire for pergola Kiwi Garden




View of fencing with locally available material at Hija village

Statement showing the beneficiaries list of the project "Establishment of Kiwi garden at Dura Morey of Ziro" under NEC scheme during 2015-16

1. Beneficiaries list of cultivation of Kiwi

Sl.No.	Name of beneficiaries	Village	Location	Area	Remarks
1.	Shri Haj Koyang	Hija	Hija	3 Ha	completed
2.	Smt. Haj Moku	Hija	Hija	3Ha	completed
3.	Smt Haj Yayung	Hija	Hija	3Ha	completed
4.	Miss Haj Rina	Hija	Hija	3ha	completed
5.	Smt. Haj Mamung	Hija	Hija	3Ha	completed
		Total		15 Ha	

(H.D.)



 District Horticulture Officer
 Lower Subansiri District, Ziro

**Statement showing the beneficiaries list of the project "Establishment of Kiwi garden at Dura Morey of Ziro" under NEC scheme during 2012-13
(1st Installment)**

1. Beneficiaries list of cultivation of Kiwi

Sl.No.	Name of beneficiaries	Village	Location	Area	Remarks
1.	Shri Puna Tai	Hija	Hija	6 Ha	completed
2.	Shri Puna Gyati	Hija	Hija	5 Ha	completed
3.	Shri Puna Ado	Hija	Hija	5 Ha	completed
4.	Smt Puna Yassung	Hija	Hija	5 ha	completed
5.	Smt. Kago Yallung	Hija	Hija	1Ha	completed
6.	Miss Puna Sumpi	Hija	Hija	1Ha	completed
7.	Smt. Kago Yallung	Hija	Hija	1Ha	completed
8.	Smt. Puna Yanya	Hija	Hija	4 Ha	completed
9.	Miss Puna Diming	Hija	Hija	3 Ha	completed
		Total		31 Ha	


(HDO)


District Horticulture Officer
Lower Subansiri District, Ziro
