

Success Story Report of Completed projects during FY 2026-27
Agri & Allied Sector, NEC

<u>Sl. No.</u>	<u>Particulars</u>	<u>Details</u>
1.	Name of the project	: Proposal of identified block for providing key identified service at Chinthong Block, Hamren, West Karbi Anglong District Assam
•	Location	: Chinthong Block, Hamren, West Karbi Anglong District Assam
•	Original AFS amount & date	: Rs. 461.20 lakh dated 30.03.2022
•	Revised AFS amount & date	: Rs. 461.19890 lakh dated 19.05.2026
•	Implementing Agency	: District Rural Development Agency (DRDA), Karbi Anglong, Assam
•	Completion date	: 31.01.2026 (As per PCR)
•	Key objective of the project	: (i) To provide employment, income opportunities and to generate skilled youths and farmers. (ii) To generate employment through farm-based activities. (iii) To generate livelihood income through market sheds by selling their local produce
•	Outcome	: Key achievements/Output/Expected Outcomes of the project are as under: • Pig sties (10 units for concern SHGs): Promoted income generation through piggery activities among Self-Help Groups (SHGs), Improved scientific rearing practices and better livestock management, enhanced financial stability and self-reliance of SHG members, created opportunities for small-scale entrepreneurship in rural areas. • Market sheds (7 units): Provided organized and hygienic spaces for local vendors to sell their products, improved market access for farmers and SHGs, reduced post-harvest, losses by enabling proper display and sale of goods, encouraged local trade and strengthened the rural economy. • Goat sites (2 units for SHGs): Supported diversification of livelihood through goat rearing, generated supplementary income for SHG members, improved animal health and productivity through better housing facilities • Anganwadi Centre (1 unit): Completion of the new Anganwadi Centre helps rural people particularly 0-6 years children, pregnant and lactating mothers to get nutrition food and other health care activities. • Weaving Complex (1 unit): Promoted traditional weaving skills and local craftsmanship, provided a dedicated workspace for artisans, especially women, enhanced production capacity and quality of woven products, created opportunities for income generation and preservation of cultural heritage. • Multi-Utility building for Skill & Community development (1 Unit): Served as a centre for training, skill development and community activities, facilitated capacity building programmes for youth and SHGs, strengthened social cohesion through community engagement, enabled organization of meetings, workshops and development initiatives.

- **Storage building for ginger (1 unit):** Reduced post-harvest losses of ginger through proper storage, helped farmers store produce and sell a better market prices, improved quality preservation and shelf life of ginger.
- **Solar Street lights (1 unit=15 nos):** Improved safety and security in the locality during night hours, facilitated movement and community activities after dark, promoted use of renewable energy and reduced electricity dependency, contributed to environmentally sustainable development.

The created assets / facilities will be made fully operational and will be maintained by District Rural Development Agency (DRDA), Karbi Anglong, Assam. The project will result in livelihood income generation through market sheds by selling their local produce and generate skilled youths and farmers.

Construction of Multi-Utility Building near Hamren Habe

Vetted Amount :- 63,32,000/-
Financial Progress :- 100%
Physical Progress :- 100%



Construction of Piggery sty of Langmeklu Hanse Arong

Vetted Amount :- 21,23,000/-
Financial Progress :- 100%
Physical Progress :- 100%



Construction of Piggery sty of Rasinga SHG at Langsomepi

Vetted Amount :- 21,23,000/-
Financial Progress :- 100%
Physical Progress :- 100%



Construction of Marketshed at Lumta Market (Umdap)

Vetted Amount :- 14,70,000/-
Financial Progress :- 100%
Physical Progress :- 100%



Construction of Storage Building For Ginger at Umlapher Bazar

Vetted Amount :- 14,70,000/-
Financial Progress :- 100%
Physical Progress :- 100%



Installation of Solar Light at Monjuli P.S.(15nos.)

Vetted Amount :- 8,62,000/-
Financial Progress :- 100%
Physical Progress :- 100%





Construction of Piggery sty of Tharna SHG at Umpho

Vetted Amount :- 21,23,000/-

Financial Progress :- 100%

Physical Progress :- 100%



Latitude: 25.766155
Longitude: 92.480729
Altitude: 774.17±5.49 m
Accuracy: 8.719 m
Time: 12-18-2025 11:57
Note: umpho, ninaru etu

Construction of Open Marketshed at Ambinong

Vetted Amount :- 14,70,000/-

Financial Progress :- 100%

Physical Progress :- 100%



Latitude: 25.83868
Longitude: 92.567838
Elevation: 421.32±7.71 m
Accuracy: 7.315 m
Time: 10-31-2025 08:01
Note: Ambinong market shed

Construction of Open Marketshed at Rongmandu

Vetted Amount :- 14,70,000/-

Financial Progress :- 100%

Physical Progress :- 100%



Latitude: 25.853555
Longitude: 92.522821
Elevation: 584.04±8 m
Accuracy: 6.4 m
Time: 05-05-2025 08:01
Note: Open Market shed at Rongmandu

Construction of Piggery sty of Dengjirso SHG at Rongnagar

Vetted Amount :- 21,23,000/-

Financial Progress :- 100%

Physical Progress :- 100%



Latitude: 25.76131
Longitude: 92.202137
Elevation: 867.73±44 m
Accuracy: 5.2 m
Time: 03-31-2025 14:18
Note: Rongnagar piggery sty

Construction of Piggery Sty of Tamhidi SHG at Rongjangphong Chinthong

Vetted Amount :- 21,23,000/-

Financial Progress :- 100%

Physical Progress :- 100%



Umsamukh, Assam, India
Rongjangphong Chinthong, Umsamukh, Assam
782413, India
Lat 25.904422° Long 92.34759°
Wednesday, 12/11/2025 03:41 PM GMT +05:30



Latitude: 25.776213
Longitude: 92.519413
Elevation: 740.32±3.9 m
Accuracy: 1.8 m
Time: 10-09-2025 07:19
Note: piggery farm house at umpho

Construction of Anganwadi centre at Langpampi

Vetted Amount :- 6,86,000/-

Financial Progress :- 100%

Physical Progress :- 100%



Time: 05-28-2026 14:27
Note: Anganwadi centre at Langpampi

Construction of Piggery sty of Sampri SHG at Rongcheck

Vetted Amount :- 21,23,000/-

Financial Progress :- 100%

Physical Progress :- 100%

**Construction of Goat sty for Jirnong SHG at Langparpan kramsa Gaon**

Vetted Amount :- 9,50,000/-

Financial Progress :- 100%

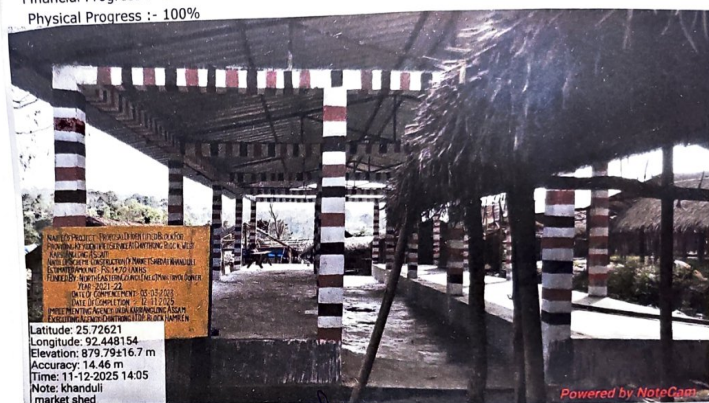
Physical Progress :- 100%

**Construction of Marketshed at Khanduli**

Vetted Amount :- 14,70,000/-

Financial Progress :- 100%

Physical Progress :- 100%

**Construction of Marketshed at Longehlobui**

Vetted Amount :- 14,70,000/-

Financial Progress :- 100%

Physical Progress :- 100%

**Construction of Piggery sty of Longre Rong Chingrum SHG at Longre**

Vetted Amount :- 21,23,000/-

Financial Progress :- 100%

Physical Progress :- 100%

**Construction of Piggery sty of Jakve Chingri Ason SHG at Habai Engti**

Vetted Amount :- 21,23,000/-

Financial Progress :- 100%

Physical Progress :- 100%

