

**GOVERNMENT OF INDIA**  
**NORTH EASTERN COUNCIL SECRETARIAT**  
**NONGRIM HILLS, SHILLONG – 793003**  
<https://necouncil.gov.in>

**Subject: Forwarding of Inspection Report.**

Inviting reference to the above subject, the physical inspection of the project **"Development Programme of Backward Block Under 30 PC Central Sector Scheme of NEC in Raishyabari R.D Block, Gandachara, Dhalai District, Tripura"**, has been carried out by Shri. Mainkumar Kharbuki, Consultant (CE) of E&M Sector and the inspection report is enclosed herewith. The project was sanctioned on 23-11-2020 at a total cost of Rs.268.0 lakh. One installment totalling Rs 107.00 lakh has been released by the NEC under "MH2552" to District Magistrate & Collector, Dhalai District, Jawaharnagar, Govt. of Tripura

The inspection report, inter alia, has mentioned that:


- On inspecting the site it could be seen that the work were in progress are as follows:
  - i. The overall progress for the Construction of Agri Sub Seed Store cum office at Tuichakma near Budha Vhar. is around 70% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - ii. The overall progress for the Construction of Agri Sub Seed Store cum office at Boakhali Bazar is around 95% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - iii. The overall progress for the Construction of Dining hall at Boakhali high School is around 70% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - iv. The overall progress for the Construction of Dining Hall at 8 No. Dyke High Schools is around 95% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
- The following work are yet to be started:
  - i. Installation & Commission of 10 KPW capacity Solar Photovoltaic Power Plant at Raishyabari PACE, Raishyabari RD Block
  - ii. Installation of SBDTW in the land of Karjyaram Tripura S/o Simnadhan Tripura of Dinaram Para under Raishyabari VC
  - iii. Installation of SBDTW in the land of Thirthabi Tripura W/o Biswamani Tripura of Balendra Para under East Potacherra VC
  - iv. Installation of SBDTW in the land of Chitya Tripura Ranjan Tripura S/o Manajoy Tripura of Mayana kumar para under Raishyabari VC
  - v. Installation of Sab Laboratory at Girish Chandra KP High School at Tuichakma VC under Raishyabari RD Block
  - vi. Construction of Market Stall (RCC Roof) at Raishyabari Bazar under Raishyabari VC
  - vii. Construction of Toilet Blocks, wash basin & Creating Wall painting at Prashanna Para Awc
  - viii. Construction of Toilet Blocks Wash basin & Creating Wall Painting at Manajoy Para Awc
  - ix. Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Jatindra Para Awc.





- x. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Maniram Para Awc.
  - xi. Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Rajchandra Para Awc.
  - xii. Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandradas Para Awc.
  - xiii. Construction of toilet Blocks, Wash Basin & Creating Wall Painting at Bijoy Para Aw, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandra Dayal Para Awc.
  - xiv. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Krishna Sakha Para awc
  - xv. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Jal Kumar Para.
  - xvi. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Nitya Kumar Para.
  - xvii. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Desarai Para Awc.
  - xviii. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Sadhan Jamatia Para.
  - xix. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Daya Ram Para Awc.
  - xx. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandra Kumar Para Awc.
  - xxi. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Darmaram Para Awc.
  - xxii. Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandidas Para Awc.
- Since the work had been implemented only in few places amounting to Rs.5134204 which is only around 47- 48 % of the first installment release. Hence we can say that the physical progress is not commensurate with the financial progress.
  - The concerned sector may seek clarification on the above observations.
  - A signboard acknowledging NEC funding was not found at site.

Enclosure: As above

  
 (Smt. Laysang Angmu Lama)  
 Director, (E&M)

U.O. No.NEC/EM/INSPECTION/AGRI&ALLIED/2021/67

To,

Adviser (Horti), NEC

Copy to,

1. P.A to Planning Adviser, NEC for kind information of Planning Adviser.
2. Sr. T.D, NIC-NEC (Shri M. Nongkhlaw) for uploading the report with photograph on NEC website.

**GOVERNMENT OF INDIA  
NORTH EASTERN COUNCIL SECRETARIAT  
NONGRIM HILLS, SHILLONG – 793003  
<https://necouncil.gov.in>**

Dated:- 7/11/2022

To  
Director (E &M),  
North Eastern Council Secretariat,  
Nongrim Hill, Shillong.

**Subject:** Submission of Inspection Report of NEC funded project titled “**Development Programme of Backward Block Under 30 PC Central Sector Scheme of NEC in Raishyabari R.D Block, Gandachara, Dhalai District, Tripura**”.

I Mainkuparkharbuki, Consultant (CE) have done the Physical Inspection of the project “**Development Programme of Backward Block Under 30 PC Central Sector Scheme of NEC in Raishyabari R.D Block, Gandachara, Dhalai District, Tripura**”.”. The project was sanctioned on 23- 11- 2020 and 15-04-2021 at a total cost of of Rs.268.0 lakhs (NEC's share 100%). One instalments totalling Rs 107.00lakh was released by the NEC, Under “2552”

**Objective of the Project:-**

- Renovation and installation of 11 KV vacuum circuit breakers of 33.11 KV sub – station at paradise para under Raishyabari VC.
- Installation & Commissioning of @KPV capacity Solar Photovoltaic power at Thakuracherre VC/Tuichakma VC/ Narikei Kunja VC/ Raima VC/ Boakhali.
- Installation & Commission of 10 KPV capacity solar Photovoltaic Power plant at Raishyabari PACE, Raishyabari Primary Health Centre.
- Installation & Commission of 10 KPV capacity Solar Photovoltaic Power Plant at Raishyabari PACE, Raishyabari RD Block.
- Installation of SBDTW in the land of Karjyaram Tripura S/o Simnadhan Tripura of Dinaram Para under Raishyabari VC.
- Installation of SBDTW in the land of Thirthabi Tripura W/o Biswamani Tripura of Balendra Para under East Potacherra VC.
- Installation of SBDTW in the land of Chitya Tripura Ranjan Tripura S/o Manajoy Tripura of Mayana kumar para under Raishyabari VC.
- Construction of Agri Sub Seed Store cum office at Tuichakma near Budha Vhar
- Construction of Agri Sub Seed Store cum office at Boakhali Bazar.
- Construction of Dining hall at Boakhali high School under Raishyabari RD Block





- Installation of Sab Laboratory at Girish Chandra KP High School at Tuichakma VC under Raishyabari RD Block
- Construction of Dining Hall at 8 No. Dyke High School
- Construction of Market Stall (RCC Roof) at Raishyabari Bazar under Raishyabari VC
- Construction of Toilet Blocks, wash basin & Creating Wall painting at Prashanna Para Awc.
- Construction of Toilet Blocks Wash basin & Creating Wall Painting at Manajoy Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Jatindra Para Awc
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Maniram Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Rajchandra Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandradas Para Awc.
- Construction of toilet Blocks, Wash Basin & Creating Wall Painting at Bijoy Para Awc
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandra Dayal Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Krishna Sakha Para awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Jal Kumar Para
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Nitya Kumar Para.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Desarai Para Awc
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Sadhan Jamatia Para.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Daya Ram Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandra Kumar Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Darmaram Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandidas Para Awc.

**Indication of Works as per DPR:-**

- Renovation and installation of 11 KV vacuum circuit breakers of 33.11 KV sub – station at paradise para under Raishyabari VC.

- Installation & Commissioning of @KPW capacity Solar Photovoltaic power at Thakuracherre VC/Tuichakma VC/ Narikei Kunja VC/ Raima VC/ Boakhali.
- Installation & Commission of 10 KPW capacity solar Photovoltaic Power plant at Raishyabari PACE, Raishyabari Primary Health Centre.
- Installation & Commission of 10 KPW capacity Solar Photovoltaic Power Plant at Raishyabari PACE, Raishyabari RD Block.
- Installation of SBDTW in the land of Karjaram Tripura S/o Simnadhan Tripura of Dinaram Para under Raishyabari VC.
- Installation of SBDTW in the land of Thirthabi Tripura W/o Biswamani Tripura of Balendra Para under East Potacherra VC.
- Installation of SBDTW in the land of Chitya Tripura Ranjan Tripura S/o Manajoy Tripura of Mayana kumar para under Raishyabari VC.
- Construction of Agri Sub Seed Store cum office at Tuichakma near Budha Vhar
- Construction of Agri Sub Seed Store cum office at Boakhali Bazar.
- Construction of Dining hall at Boakhali high School under Raishyabari RD Block
- Installation of Sab Laboratory at Girish Chandra KP High School at Tuichakma VC under Raishyabari RD Block
- Construction of Dining Hall at 8 No. Dyke High School
- Construction of Market Stall (RCC Roof) at Raishyabari Bazar under Raishyabari VC
- Construction of Toilet Blocks, wash basin & Creating Wall painting at Prashanna Para Awc.
- Construction of Toilet Blocks Wash basin & Creating Wall Painting at Manajoy Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Jatindra Para Awc
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Maniram Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Rajchandra Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandradas Para Awc.
- Construction of toilet Blocks, Wash Basin & Creating Wall Painting at Bijoy Para Awc
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandra Dayal Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Krishna Sakha Para awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Jal Kumar Para



- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Nitya Kumar Para.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Desarai Para Awc
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Sadhan Jamatia Para.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Daya Ram Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandra Kumar Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Darmaram Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandidas Para Awc.

**Proposed Outcome of the project:-**

Establishment of infrastructure development in the district.

**Observation mentioned in inspection report:**

- The Consultants had inspected the project "Development Programme of Backward Block Under 30 PC Central Sector Scheme of NEC in Raishyabari R.D Block, Gandachara, Dhalai District, Tripura".
- On inspecting the site it could be seen that the work were in progress are as follows:
  - i. The overall progress for the Construction of Agri Sub Seed Store cum office at Tuichakma near Budha Vhar. is around 70% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - ii. The overall progress for the Construction of Agri Sub Seed Store cum office at Boakhali Bazar is around 95% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - iii. The overall progress for the Construction of Dining hall at Boakhali high School is around 70% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - iv. The overall progress for the Construction of Dining Hall at 8 No. Dyke High School is around 95% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
- The work related to Installation & Commission of 10 KPW capacity Solar Photovoltaic Power Plant at Raishyabari PACE, Raishyabari RD Block, Installation of SBDTW in the land of Karjyaram Tripura S/o Simnadhan Tripura of Dinaram Para under Raishyabari VC, Installation of SBDTW in the land of Thirthabi Tripura W/o Biswamani Tripura of Balendra Para under East Potacherra VC, Installation of SBDTW in the land of Chitya

Tripura Ranjan Tripura S/o Manajoy Tripura of Mayana kumar para under Raishyabari VC, Installation of Sab Laboratory at Girish Chandra KP High School at Tuichakma VC under Raishyabari RD Block, Construction of Market Stall (RCC Roof) at Raishyabari Bazar under Raishyabari VC, Construction of Toilet Blocks, wash basin & Creating Wall painting at Prashanna Para Awc, Construction of Toilet Blocks Wash basin & Creating Wall Painting at Manajoy Para Awc, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Jatindra Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Maniram Para Awc, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Rajchandra Para Awc, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandradas Para Awc, Construction of toilet Blocks, Wash Basin & Creating Wall Painting at Bijoy Para Aw, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandra Dayal Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Krishna Sakha Para awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Jal Kumar Para, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Nitya Kumar Para, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Desarai Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Sadhan Jamatia Para, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Daya Ram Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandra Kumar Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Darmaram Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandidas Para Awc are yet to be started.

- Since the work had been implemented only in few places amounting to **Rs.5134204** which is only around **47- 48 %** of the first installment release. Hence we can say that the physical progress is not commensurate with the financial progress.
- The concerned sector may seek clarification on the above observations.
- A signboard acknowledging NEC funding was not found at site.



(Mainkumar Kharbuki)

Consultant (CE)

NEC, Secretariat, Shillong



**Report of the inspection carried from 30/10/2022 to 02/11/2022 for the NEC funded project "Development Programme of Backward Block Under 30 PC Central Sector Scheme of NEC in Raishyabari R.D Block, Gandachara, Dhalai District, Tripura.**

An inspection of the above project was carried out by the Consultants of E&M Sector, NEC Secretariat, Shillong alongwith the officials of District Magistrate & Collector, Dhalai District, Jawaharnagar, Govt. of Tripura from **30/10/2022 to 02/11/2022**. The list of the officials present during the inspection is enclosed as Annexure-I & The photographs taken during the time of inspection is enclosed as Annexure-II.

**(I) BACKGROUND:**

Name of the project:	Development Programme of Backward Block Under 30 PC Central Sector Scheme of NEC in Raishyabari R.D Block, Gandachara, Dhalai District, Tripura.
Location:	Raishyabari block, Dhalai district: Jawaharnagar, Tripura
Implementing Agency:	District Magistrate & Collector, Dhalai District, Jawaharnagar, Govt. of Tripura
Date of Approval	23-11-2020
Date of Sanction:	23- 11- 2020 and 15-04-2021
Cost of Project:	Rs.268.00lakh
NEC Share (100%):	Rs.268.00 lakh
NEC Share released & Dates:	Rs. 10.00 Lakh released on 23-11-2020 and Rs 97.00 lakh released on 15-04- 2021 of 1 <sup>st</sup> Installment
Total Amount Released:	Rs 107.00lakh
Balance amount to be released by NEC:	Rs.161.00lakh
Status of UC for NEC share:	Rs. 107.00 lakh
Target Date of Completion:	23-11- 2022
Time Overrun	NA

**(II) Aim/Objective of the Project:**

- Renovation and installation of 11 KV vacuum circuit breakers of 33.11 KV sub – station at paradise para under Raishyabari VC.
- Installation & Commissioning of @KPW capacity Solar Photovoltaic power at Thakuracherre VC/Tuichakma VC/ Narikei Kunja VC/ Raima VC/ Boakhali.
- Installation & Commission of 10 KPW capacity solar Photovoltaic Power plant at Raishyabari PACE, Raishyabari Primary Health Centre.

*Maitrayee Khatun*



- Installation & Commission of 10 KPW capacity Solar Photovoltaic Power Plant at Raishyabari PACE, Raishyabari RD Block.
- Installation of SBDTW in the land of Karjyaram Tripura S/o Simnadhan Tripura of Dinaram Para under Raishyabari VC.
- Installation of SBDTW in the land of Thirthabi Tripura W/o Biswamani Tripura of Balendra Para under East Potacherra VC.
- Installation of SBDTW in the land of Chitya Tripura Ranjan Tripura S/o Manajoy Tripura of Mayana kumar para under Raishyabari VC.
- Construction of Agri Sub Seed Store cum office at Tuichakma near Budha Vhar
- Construction of Agri Sub Seed Store cum office at Boakhali Bazar.
- Construction of Dining hall at Boakhali high School under Raishyabari RD Block
- Installation of Sab Laboratory at Girish Chandra KP High School at Tuichakma VC under Raishyabari RD Block
- Construction of Dining Hall at 8 No. Dyke High School
- Construction of Market Stall (RCC Roof) at Raishyabari Bazar under Raishyabari VC
- Construction of Toilet Blocks, wash basin & Creating Wall painting at Prashanna Para Awc.
- Construction of Toilet Blocks Wash basin & Creating Wall Painting at Manajoy Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Jatindra Para Awc
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Maniram Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Rajchandra Para Awc.
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandradas Para Awc.
- Construction of toilet Blocks, Wash Basin & Creating Wall Painting at Bijoy Para Awc
- Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandra Dayal Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Krishna Sakha Para awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Jal Kumar Para
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Nitya Kumar Para.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Desarai Para Awc
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Sadhan Jamatia Para.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Daya Ram Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandra Kumar Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Darmaram Para Awc.
- Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandidas Para Awc.


  
Manikumar Bhattacharya

**(III) Outcomes of the Project:**

Establishment of infrastructure development in the district.

**(IV) Observations/ Status of works:**

Sl. no.	Approved Items of works mention in DPR.	Quantity	Accepted Cost as per NEC tech. Vetting (Rs in Lakhs)	Remarks
1	Renovation and installation of 11 KV vacuum circuit breakers of 33.11 KV sub – station at paradise para under Raishyabari VC.	4	16,63,000.00	• Not yet started
2	Installation & Commissioning of @KPW capacity Solar Photovoltaic power at Thakuracherre VC/Tuichakma VC/ Narikei Kunja VC/ Raima VC/ Boakhali.	7	65,58,258.00	• Not yet started
3	Installation & Commission of 10 KPW capacity solar Photovoltaic Power plant at Raishyabari PACE, Raishyabari Primary Health Centre.	1	17,71,463.00	• Not yet started
4	Installation & Commission of 10 KPW capacity Solar Photovoltaic Power Plant at Raishyabari PACE, Raishyabari RD Block.	1	17,71,463.00	• Not yet started
5	Installation of SBDTW in the land of Karjyaram Tripura S/o Simnadhan Tripura of Dinaram Para under Raishyabari VC.	1	12.96,640.00	• Not yet started
6	Installation of SBDTW in the land of Thirthabi Tripura W/o Biswamani Tripura of Balendra Para under East Potacherra VC.	1		• Not yet started
7	Installation of SBDTW in the land of Chitya Tripura Ranjan Tripura S/o Manajoy Tripura of Mayana	1		• Not yet started

  
Mainupur



	kumar para under Raishyabari VC.			
8	Construction of Agri Sub Seed Store cum office at Tuichakma near Budha Vhar.	1	17,09,534.70	<ul style="list-style-type: none"> <li>• During inspection it was found out that the construction works is in progress.</li> <li>• The plinth area of Agri Sub Seed Store cum office is 116.875 sqm (12.5 x9.35 m).Earthworks, RCC work , Brick workhave been completed.</li> <li>• Wood and PVC work, Steel work, CC work, flooring and skirting work, Plastering, Painting, Roof Truss, Roofing &amp; ceiling works,finishing work and Electrical works are yet to be started.</li> </ul>
9	Construction of Agri Sub Seed Store cum office at Boakhali Bazar.	1	17,09,534.70	<ul style="list-style-type: none"> <li>• During inspection it was found out that the construction works is in progress.</li> <li>• The plinth area of Agri Sub Seed Store cum office at Boakhali Bazar is 117.03 sqm (12.45x9.4m).</li> <li>• Earthworks, RCC work , CC work, Brick work, Wood and PVC work, Steel work, flooring and skirting work, Plastering, Painting, Roof Truss, Roofing &amp; ceiling works, finishing work have been completed.</li> <li>• Flooring and skirting work inside could not inspect as it was locked.</li> <li>• Electrical works are yet to be started.</li> </ul>
10	Construction of Dining hall at Boakhali high School under Raishyabari RD Block.	1	16,05,518.15	<ul style="list-style-type: none"> <li>• During inspection it was found out that the construction works is in progress.</li> <li>• The plinth area of Dining hall at Boakhali high school is 113.925 sqm (14.7x7.75 m). Earthwork, RCC work, Brickwork have been completed,</li> <li>• Wood and PVC work, Steel work, CC work, flooring and skirting work, Plastering, Painting, Roof Truss, Roofing &amp; ceiling works,finishing work, sanitary installations, water supply, sewage and drainage work, Electrical worksare yet to be started..</li> </ul>
11	Installation of Sab Laboratory at Girish Chandra KP High School at Tuichakma VC under Raishyabari RD Block.	1	2,56,445.00	<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
12	Construction of Dining Hall at 8 No. Dyke High School.	1	12,52,219.9	<ul style="list-style-type: none"> <li>• During inspection it was found out that the construction works is in progress.</li> </ul>

  
Mainup  
tehran

				<ul style="list-style-type: none"> <li>• The plinth area of Dining Hall at 8 No. Dyke High School is 92.04 sqm (11.8x 7.8 m).</li> <li>• Foundation works, Erection of column, CC Flooring, Brick Walling, Wood and PVC work, Steel work, CC work, Plastering, Painting, Roof Truss, Roofing &amp; ceiling works, finishing work have been completed.</li> <li>• flooring and skirting work inside could not inspect as it was locked.</li> <li>• Sanitary installations, water supply, sewage and drainage work, Electrical works are yet to be started.</li> </ul>
13	Construction of Market Stall (RCC Roof) at Raishyabari Bazar under Raishyabari VC.	1	47,58,000.00	<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
14	Construction of Toilet Blocks, wash basin & Creating Wall painting at Prashanna Para Awc.	1	16,85,798.00	<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
15	Construction of Toilet Blocks Wash basin & Creating Wall Painting at Manajoy Para Awc.	1		<ul style="list-style-type: none"> <li>• Not yet Started</li> </ul>
16	Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Jatindra Para Awc.	1		<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
17	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Maniram Para Awc.	1		<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
18	Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Rajchandra Para Awc.	1		<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
19	Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandradas Para Awc.	1		<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
20	Construction of toilet Blocks, Wash Basin & Creating Wall Painting at Bijoy Para Awc.	1		<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>
21	Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandra Dayal Para Awc.	1		<ul style="list-style-type: none"> <li>• Not yet started</li> </ul>

  
 Maiburn  
 Maiburn



22	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Krishna Sakha Para awc.	1		• Not yet started
23	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Jal Kumar Para.	1		• Not yet started
24	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Nitya Kumar Para.	1		• Not yet started
25	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Desarai Para Awc.	1		• Not yet started
26	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Sadhan Jamatia Para.	1		• Not yet started
27	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Daya Ram Para Awc.	1		• Not yet started
28	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandra Kumar Para Awc.	1		• Not yet started
29	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Darmaram Para Awc.	1		• Not yet started
30	Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandidas Para Awc.	1		• Not yet started
	Total			2,60,37,874.
	Add 3% Contingency Charge			781,136.23
	Total	-		2,68,19,010.68
	Say	-		268.00 lakhs


  
 Mainupar  
 khuchh.

**(VI) Location:-**

Latitude	Longitude
N 23°32'1"	E 91°53'8"
N 23°27'5"	E 91°53'38"
N 23°29'27"	E 91°55'1"
N 23°29'12"	E 91°54'51"

**(VII) Overall Remarks:-**

- The Consultants had inspected the project "Development Programme of Backward Block Under 30 PC Central Sector Scheme of NEC in Raishyabari R.D Block, Gandachara, Dhalai District, Tripura".
- On inspecting the site it could be seen that the work were in progress are as follows:
  - i. The overall progress for the Construction of Agri Sub Seed Store cum office at Tuichakma near Budha Vhar is around 70% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - ii. The overall progress for the Construction of Agri Sub Seed Store cum office at Boakhali Bazar is around 95% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - iii. The overall progress for the Construction of Dining hall at Boakhali High School is around 70% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
  - iv. The overall progress for the Construction of Dining Hall at 8 No. Dyke High School is around 95% of the total works. The Plinth area constructed is more or less the same as in the approved DPR.
- The work related to Installation & Commission of 10 KPW capacity Solar Photovoltaic Power Plant at Raishyabari PACE, Raishyabari RD Block, Installation of SBDTW in the land of Karjyaram Tripura S/o Simnadhan Tripura of Dinaram Para under Raishyabari VC, Installation of SBDTW in the land of Thirthabi Tripura W/o Biswamani Tripura of Balendra Para under East Potacherra VC, Installation of SBDTW in the land of Chitya Tripura Ranjan Tripura S/o Manajoy Tripura of Mayana kumar para under Raishyabari VC, Installation of Sab Laboratory at Girish Chandra KP High School at Tuichakma VC under Raishyabari RD Block, Construction of Market Stall (RCC Roof) at Raishyabari Bazar under Raishyabari VC, Construction of Toilet Blocks, wash basin & Creating Wall painting at Prashanna Para Awc, Construction of Toilet Blocks Wash basin & Creating Wall Painting at Manajoy Para Awc, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Jatindra Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Maniram Para Awc, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Rajchandra Para Awc, Construction of Toilet Blocks, Wash basin & Creating Wall Painting at Chandradas Para Awc, Construction of toilet Blocks, Wash Basin & Creating Wall Painting at Bijoy Para Aw, Construction of Toilet Blocks,

  
Maitrayon  
Kishor



Wash basin & Creating Wall Painting at Chandra Dayal Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Krishna Sakha Para awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Jal Kumar Para, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Nitya Kumar Para, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Desarai Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Sadhan Jamatia Para, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Daya Ram Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Darmaram Para Awc, Construction of Toilet Blocks, Wash Basin & Creating Wall Painting at Chandidas Para Awc are yet to be started.

- Since the work had been implemented only in few places amounting to **Rs.5134204** which is only around **47- 48 %** of the first installment release. Hence we can say that the physical progress is not commensurate with the financial progress.
- The concerned sector may seek clarification on the above observations.
- A signboard acknowledging NEC funding was not found at site.



(Mainkumar Kharbuki)  
Consultant (CE)  
NEC Secretariat, Shillong

List of officials who were present during the inspection of NEC funded project  
Development Programme of Bachward Block under 30 PC Control on ...../...../2022  
Sector Scheme of NEC in Raishyabari RD Block, Gonda Chala, Dhalai, District, Tripura








Sl. No.	Name	Contact No. & Email id	Designation & Organisation/Department	Signature
1.	Jayanta Gamatia	9717624645	BDO, Raishyabari	
2.	Smajit Reag	9366105962	ADDL BDO, Raishyabari	
3.	Ex. Paritosh Das	7629095130	SDO, RD, Gonda-Twaka	
4.	Sajal Debbarma		RPS	
5.	Dilip Kanti Das	708588853	GRS	
6.	Prabin Debbarma	9262207852	DWO, Dhalai	
7.	Manikanta Debbarma	8280054981	Consultant (CE) NEC	
8.				
9.				
10.				
11.				
12.				





Photo showing consultant along with the implementing dept. inspecting the construction of Dining hall at 8 No. Dyke High School is under progress

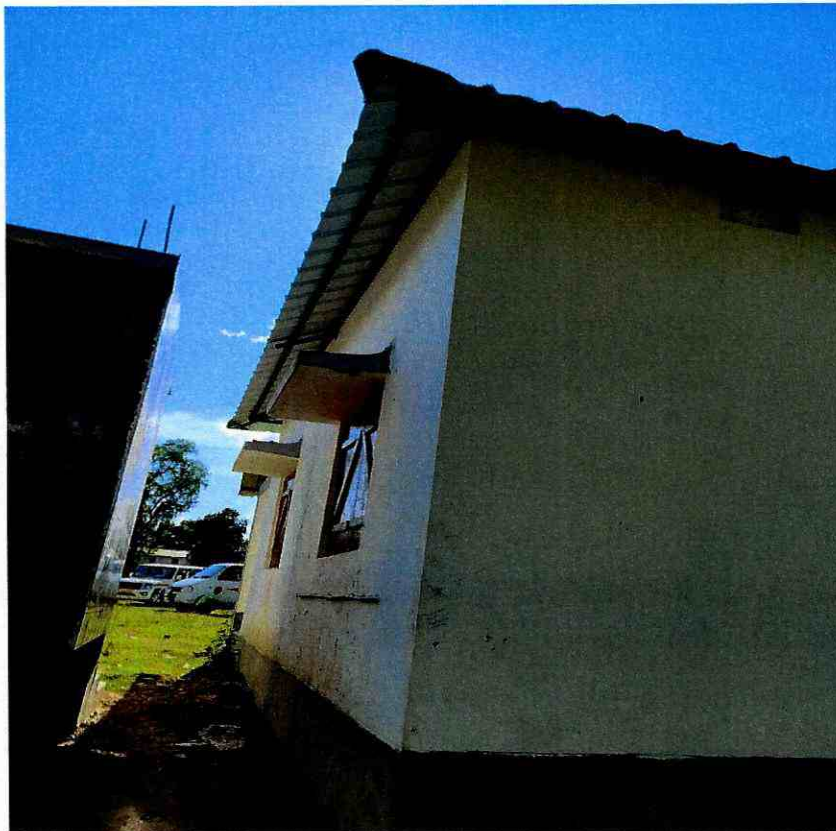


Photo showing the construction of Dining hall at 8 No. Dyke High School is under progress



Photo showing construction of Agri Sub Seed Store cum office at Tuichakma near BudhaVhar is under progress

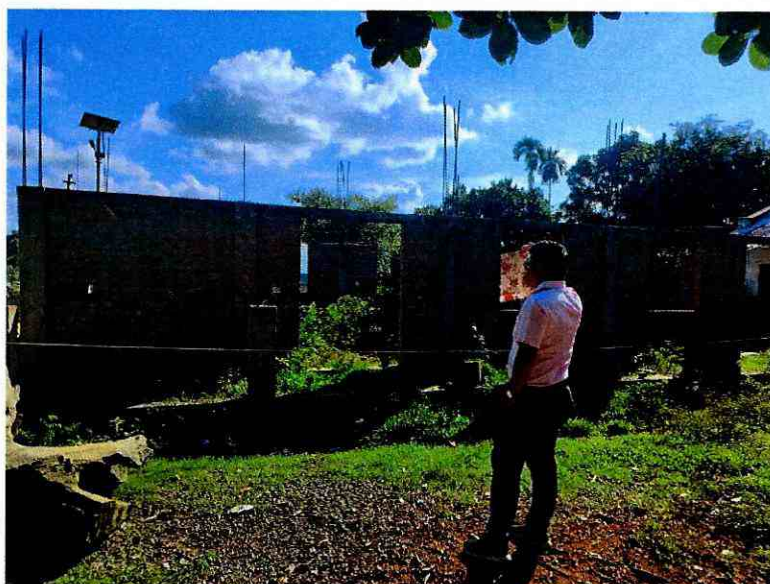


Photo showing construction of Dining hall at Boakhali High School under Raishyabari RD Block is under progress



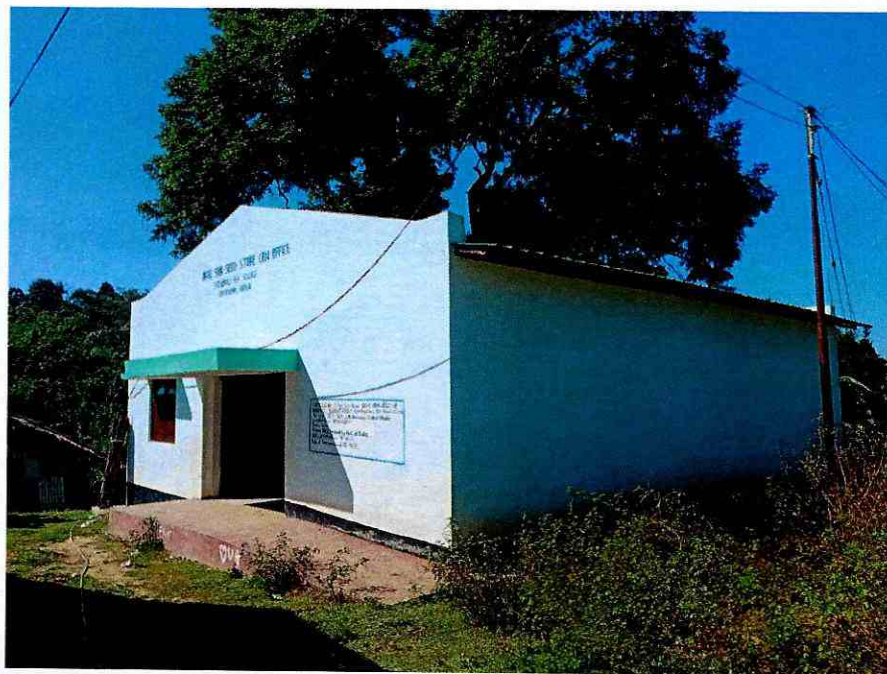


Photo showing construction of Agri Sub Seed Store cum Office at Boakhali Bazar is under progress

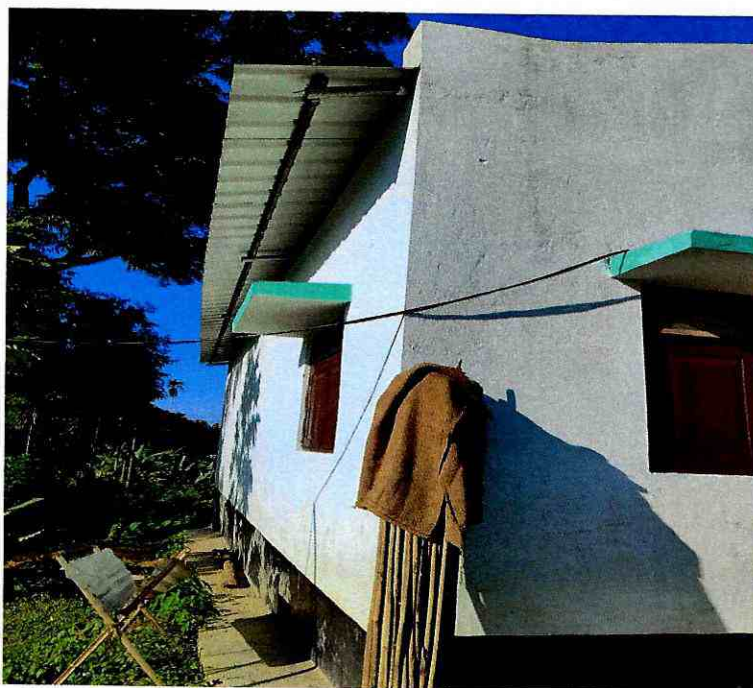


Photo showing construction of Agri Sub Seed Store cum Office at Boakhali Bazar is under progress
